

Last Transaction Date
2025-03-31

Count of Transactions
232,657

Count of Trusted Projects
24

Total Cost

4,696,850,905

Cost Type (lvl 1)



Cost Type (lvl 2)




Cost Type (lvl 3)

Materials	2,091M
Civil Subcontracts	666M
Arch Subcontracts A	591M
Site General Equipment	276M
Staff Salaries	239M
Infra Subcontracts	225M
Indirect & Service Labor...	164M
Elec Subcontracts	96M
Mech Subcontracts	72M
Mob, Demobilization & Fi...	68M
SOCIAL INSURANCE-Ma...	41M
Professional Services	26M
Staff Housing and Labou...	26M
STAMP DUTIES / Engine...	24M
Running Cost for Contra...	22M
Equipment	18M
Client Facilities	17M
Contractor's Site Faciliti...	10M
INSURANCE -Markt up a...	10M
H.S.E & Scafolding	8M
Arab Fees	4M
General Subcontracts	2M
FINANCE CHARGES	0M
Contractor's Furniture, O...	0M





Cost By Business Type

Earth Work	624.12 M
Metal works	503.03 M
Concrete Work	471.76 M
Steel Structure	297.49 M
Infra Works	178.15 M
Aluminum works	170.40 M
Equipment Rent	165.12 M
Glass Works	164.26 M
Deep Foundation & Soil ...	138.33 M
Electrical Works	85.90 M
Mechanical & Plumping	81.82 M
GRC & GRP	75.23 M
Labors	63.82 M
Precast Concrete	57.60 M
Masonry works	54.04 M
Plastering works	42.77 M
Land scape	42.17 M
Tiling works & Clay tiling	40.58 M
Finishing Works	40.19 M
Marbles Works	36.78 M
Consultancy	32.13 M
Paintings	25.85 M
Insulations & Protection	22.58 M
Dewatering	18.99 M
Gypsum Works	15.84 M
Special Flooring	15.07 M
Wooden works	9.56 M
Furniture	4.36 M
Scaffolds Erection	3.97 M
Core & Shell	1.90 M
Structure Works	1.53 M
Repair & Concrete Stre...	1.50 M

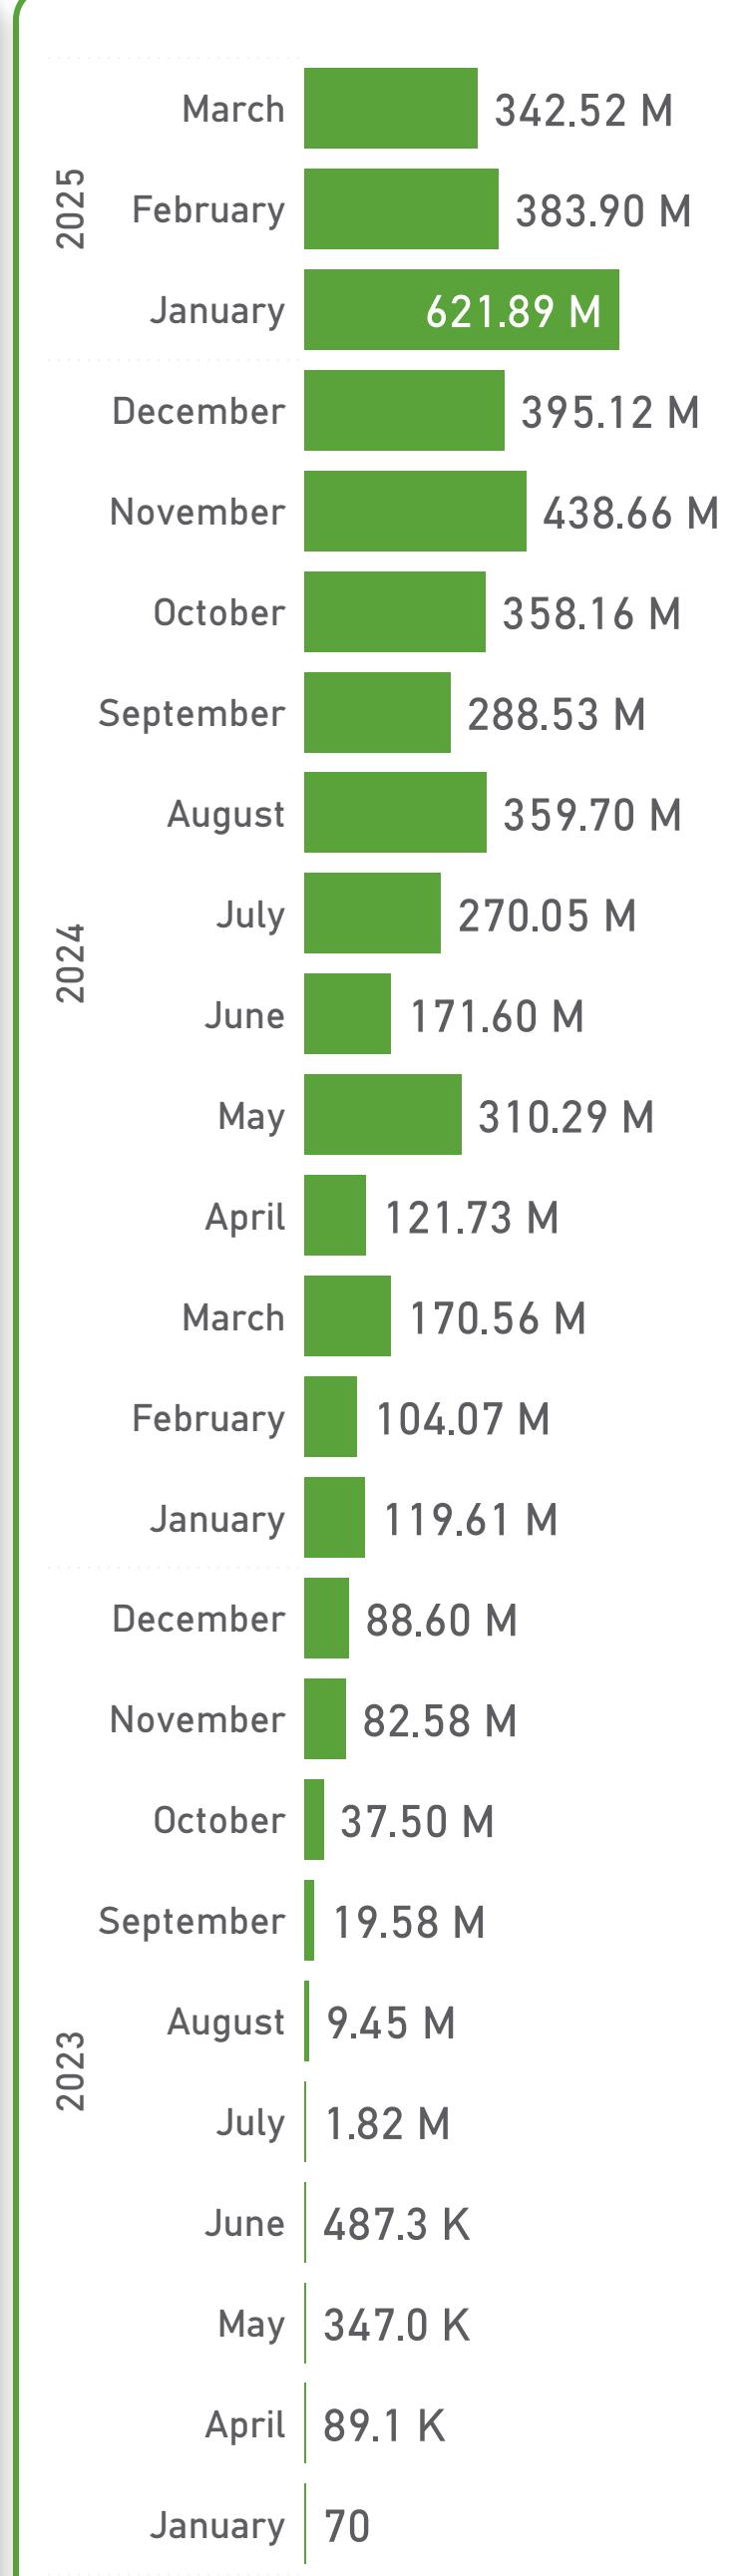

Trusted Projects

AOU Extension
Bay West Valley
Bleu Vert -25 Buildin...
Garayan
Gomla Market
GPX
Helio Square
Lagoon Park P01&P02
Marsa Baghush
Mostakbal Misr
Mostakbal Misr PS2
Mostakbal Misr PS4
Mostakbal Misr Zone5
Raville Tower
Reef Town 44 Buildin...
Sewage Networks of ...
Sherben Hospital
SILVERSANDS-Ph 1

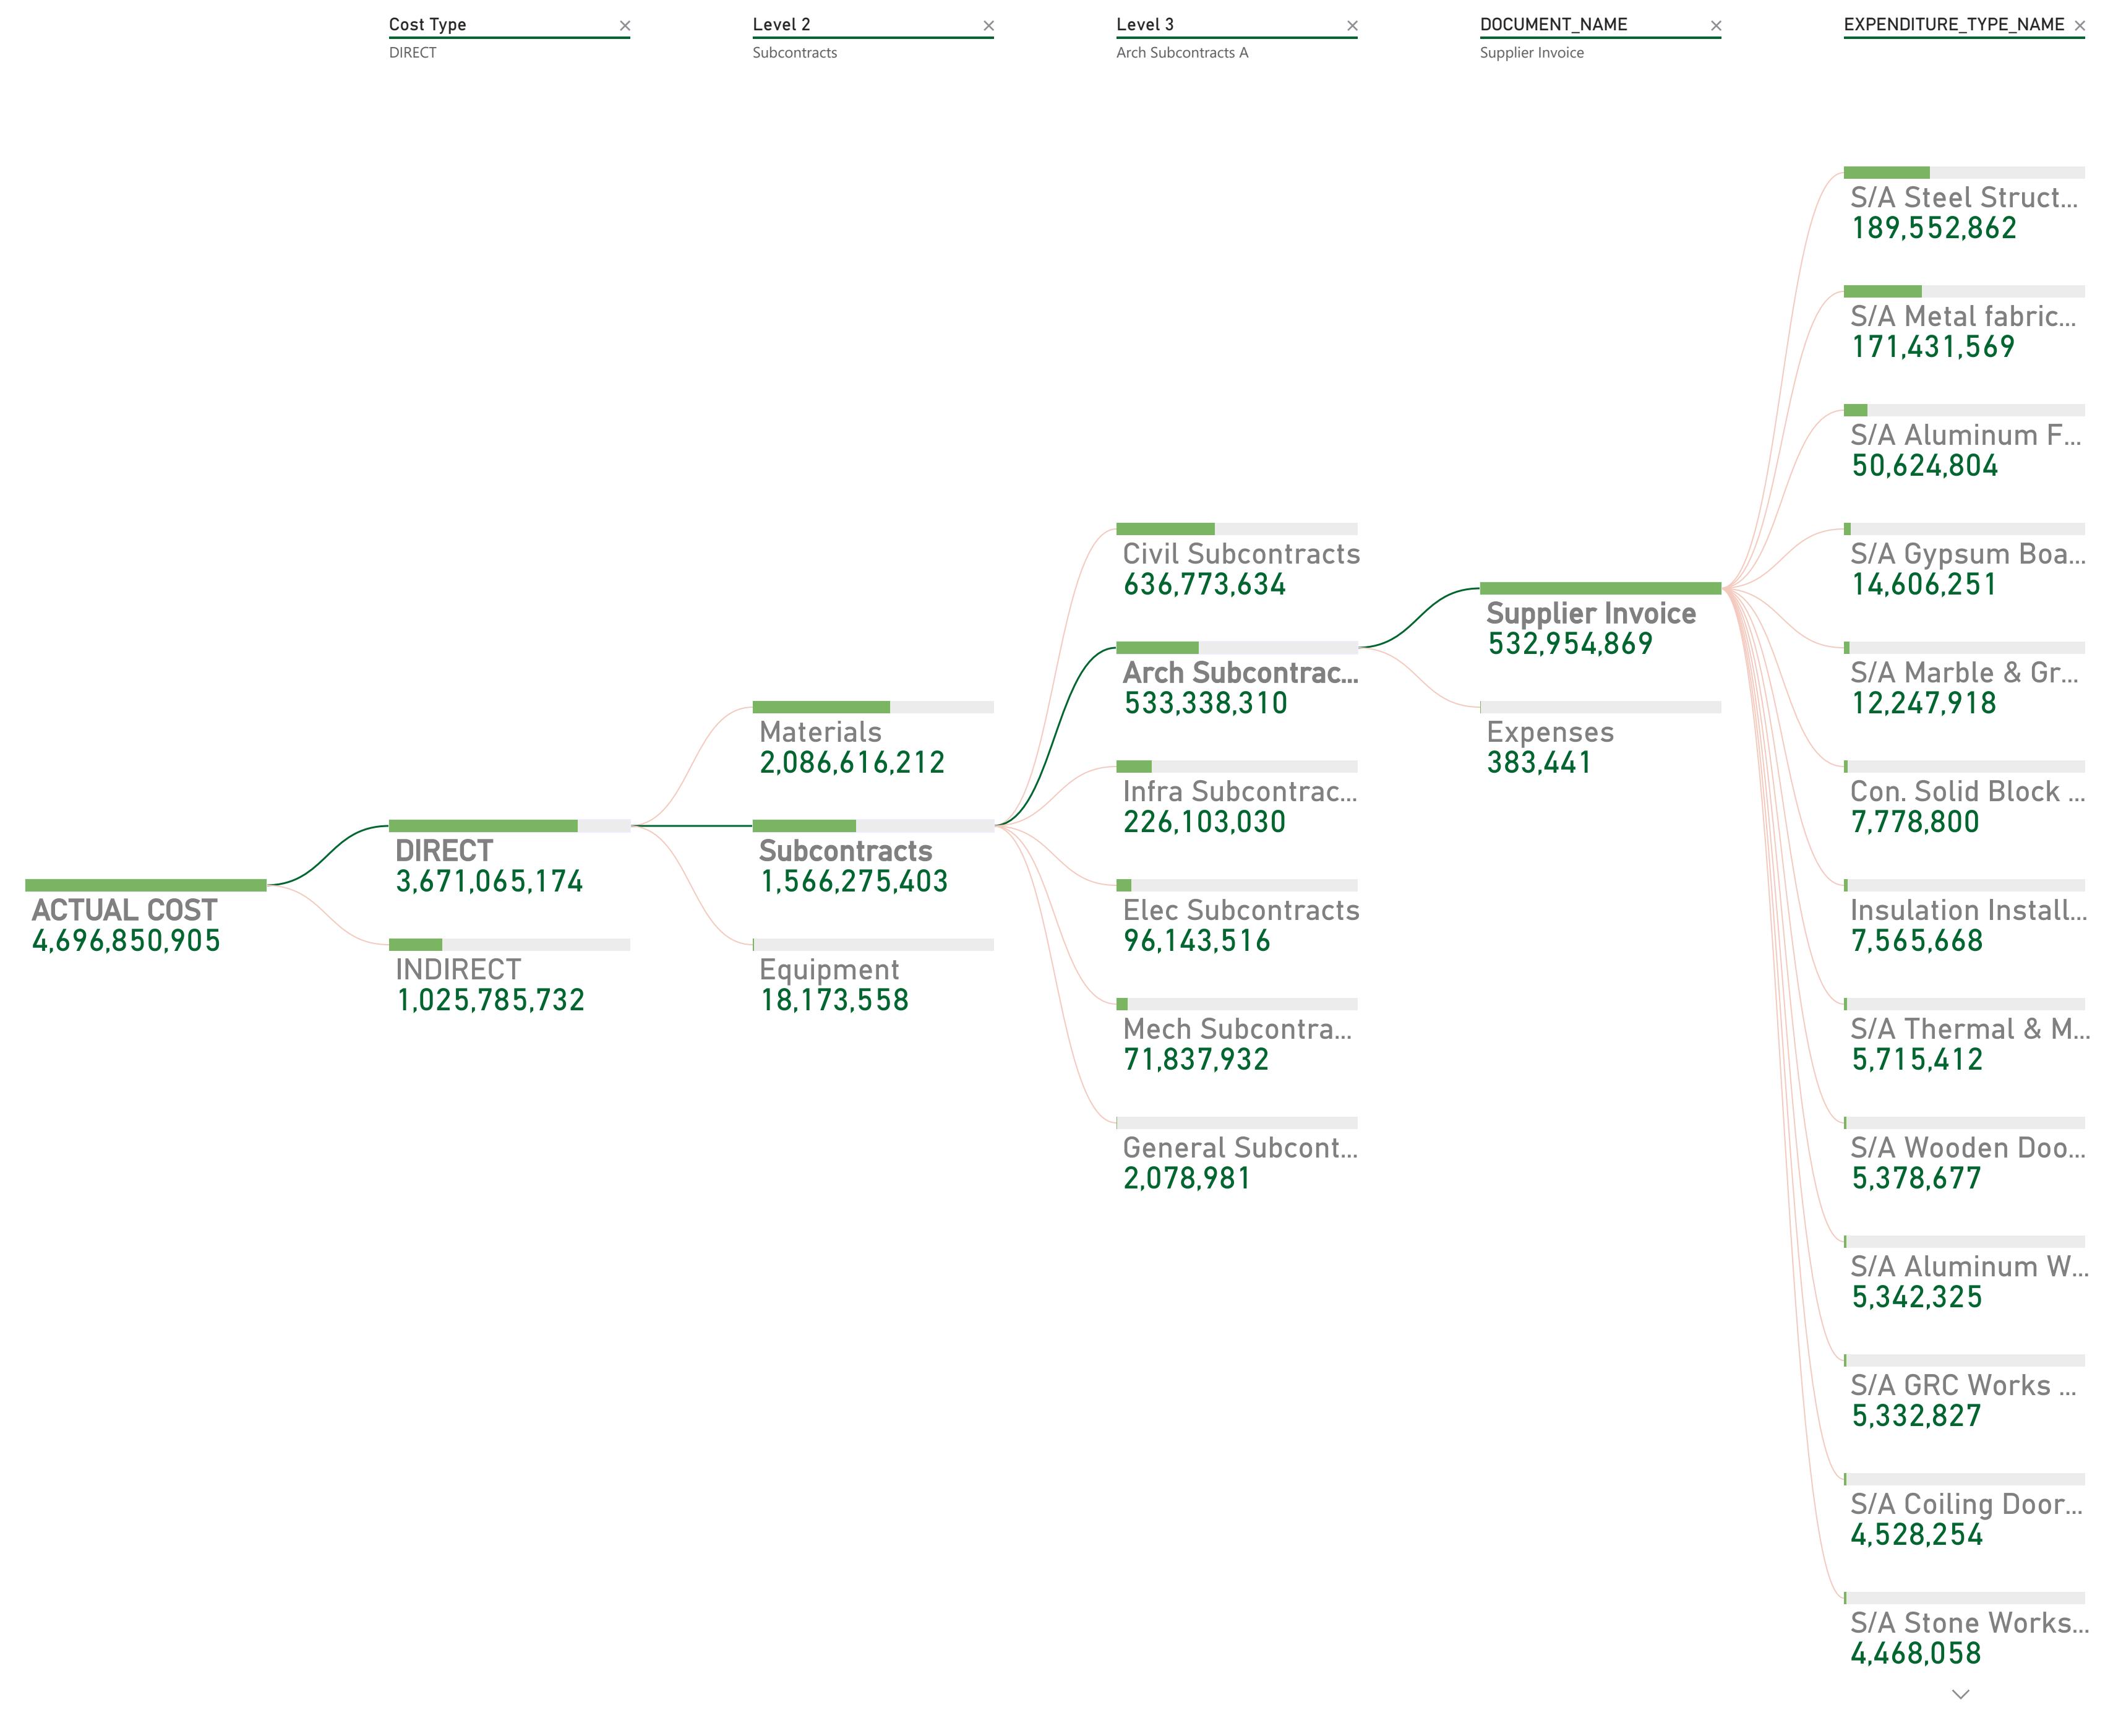



ZED EAST

August Target



Section	Buildings	Fence	Villas						
Unit Type	G3A	G3B	TH	THA	TW	VB	VC	XLA	XLC
Unit Number	All		Discipline	All					

Work Package	New Name
Cables & Wires	Annex Room Communication Cable Pulling
Ceramics	Annex Room Communication Sockets & Switches
Earthing systems	Annex Room gypsum board false ceiling Final Fix
Equipment Cabinet IEC	Annex Room lighting fixtures (By others)
External Painting	Annex Room painting 1st stage Ceiling
External Plaster	Annex Room painting 1st stage Walls
Fence Chain Link	Annex Room sockets & switches
Fence Dry-Mix	Bathtub installation
Fence Painting	
Fence Plaster	
Fence Steel Fence & Gates	
Fence Stone Clading	
Floor Distribution Boards	
Floor Drains	
Gypsum Board	
HDF	
HVAC	
Inspection Chambers & Hos...	
Internal Painting	
Internal Pipes	
Internal Plaster	
Lighting Fixtures	
Marble	
Panel Boards	
Porcelain	
Risers	
Roof Aggregate	
Roof Drains	
Roof Metal Flashing	
Sanitary Fixtures	
Stairs Handrail	
Steel Ladder Hook	
Stone Cladding	
Stone Vanity	
Terrace Drains	

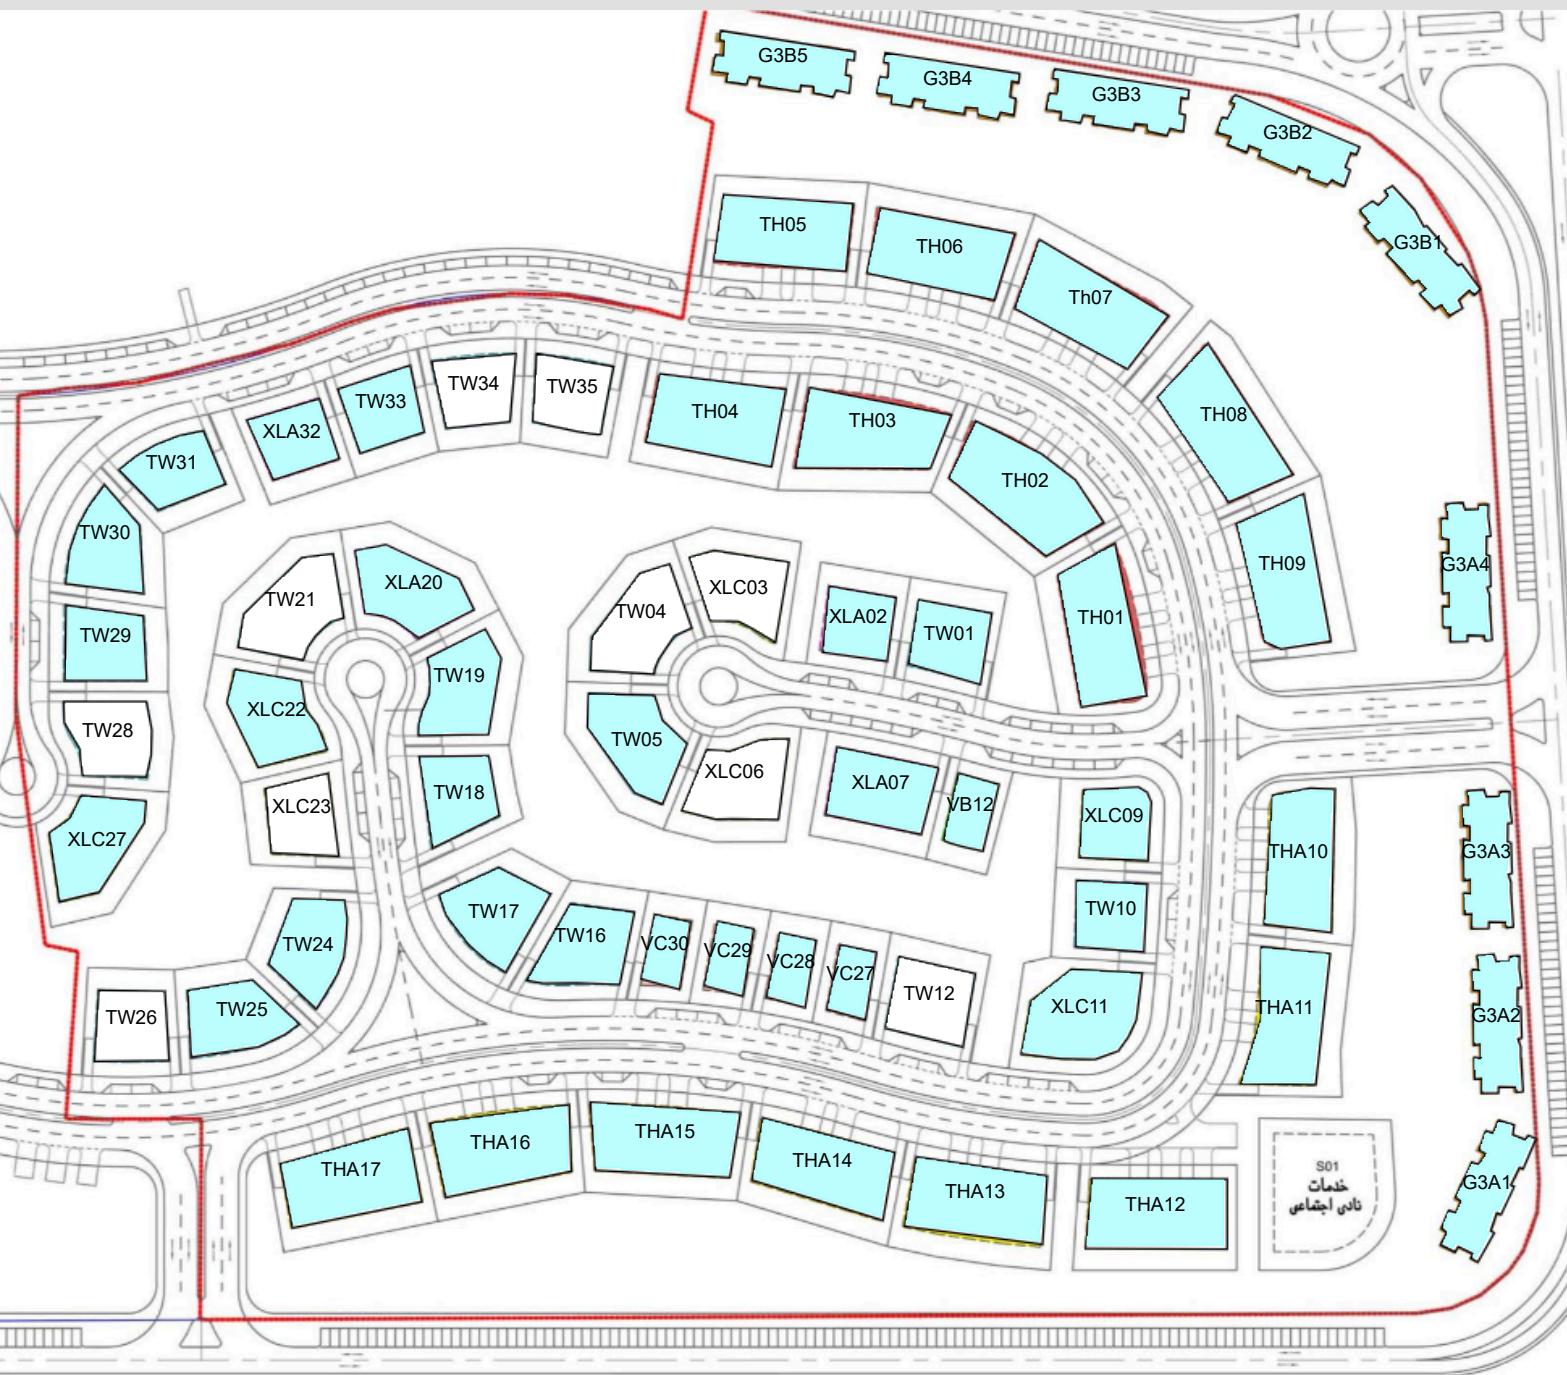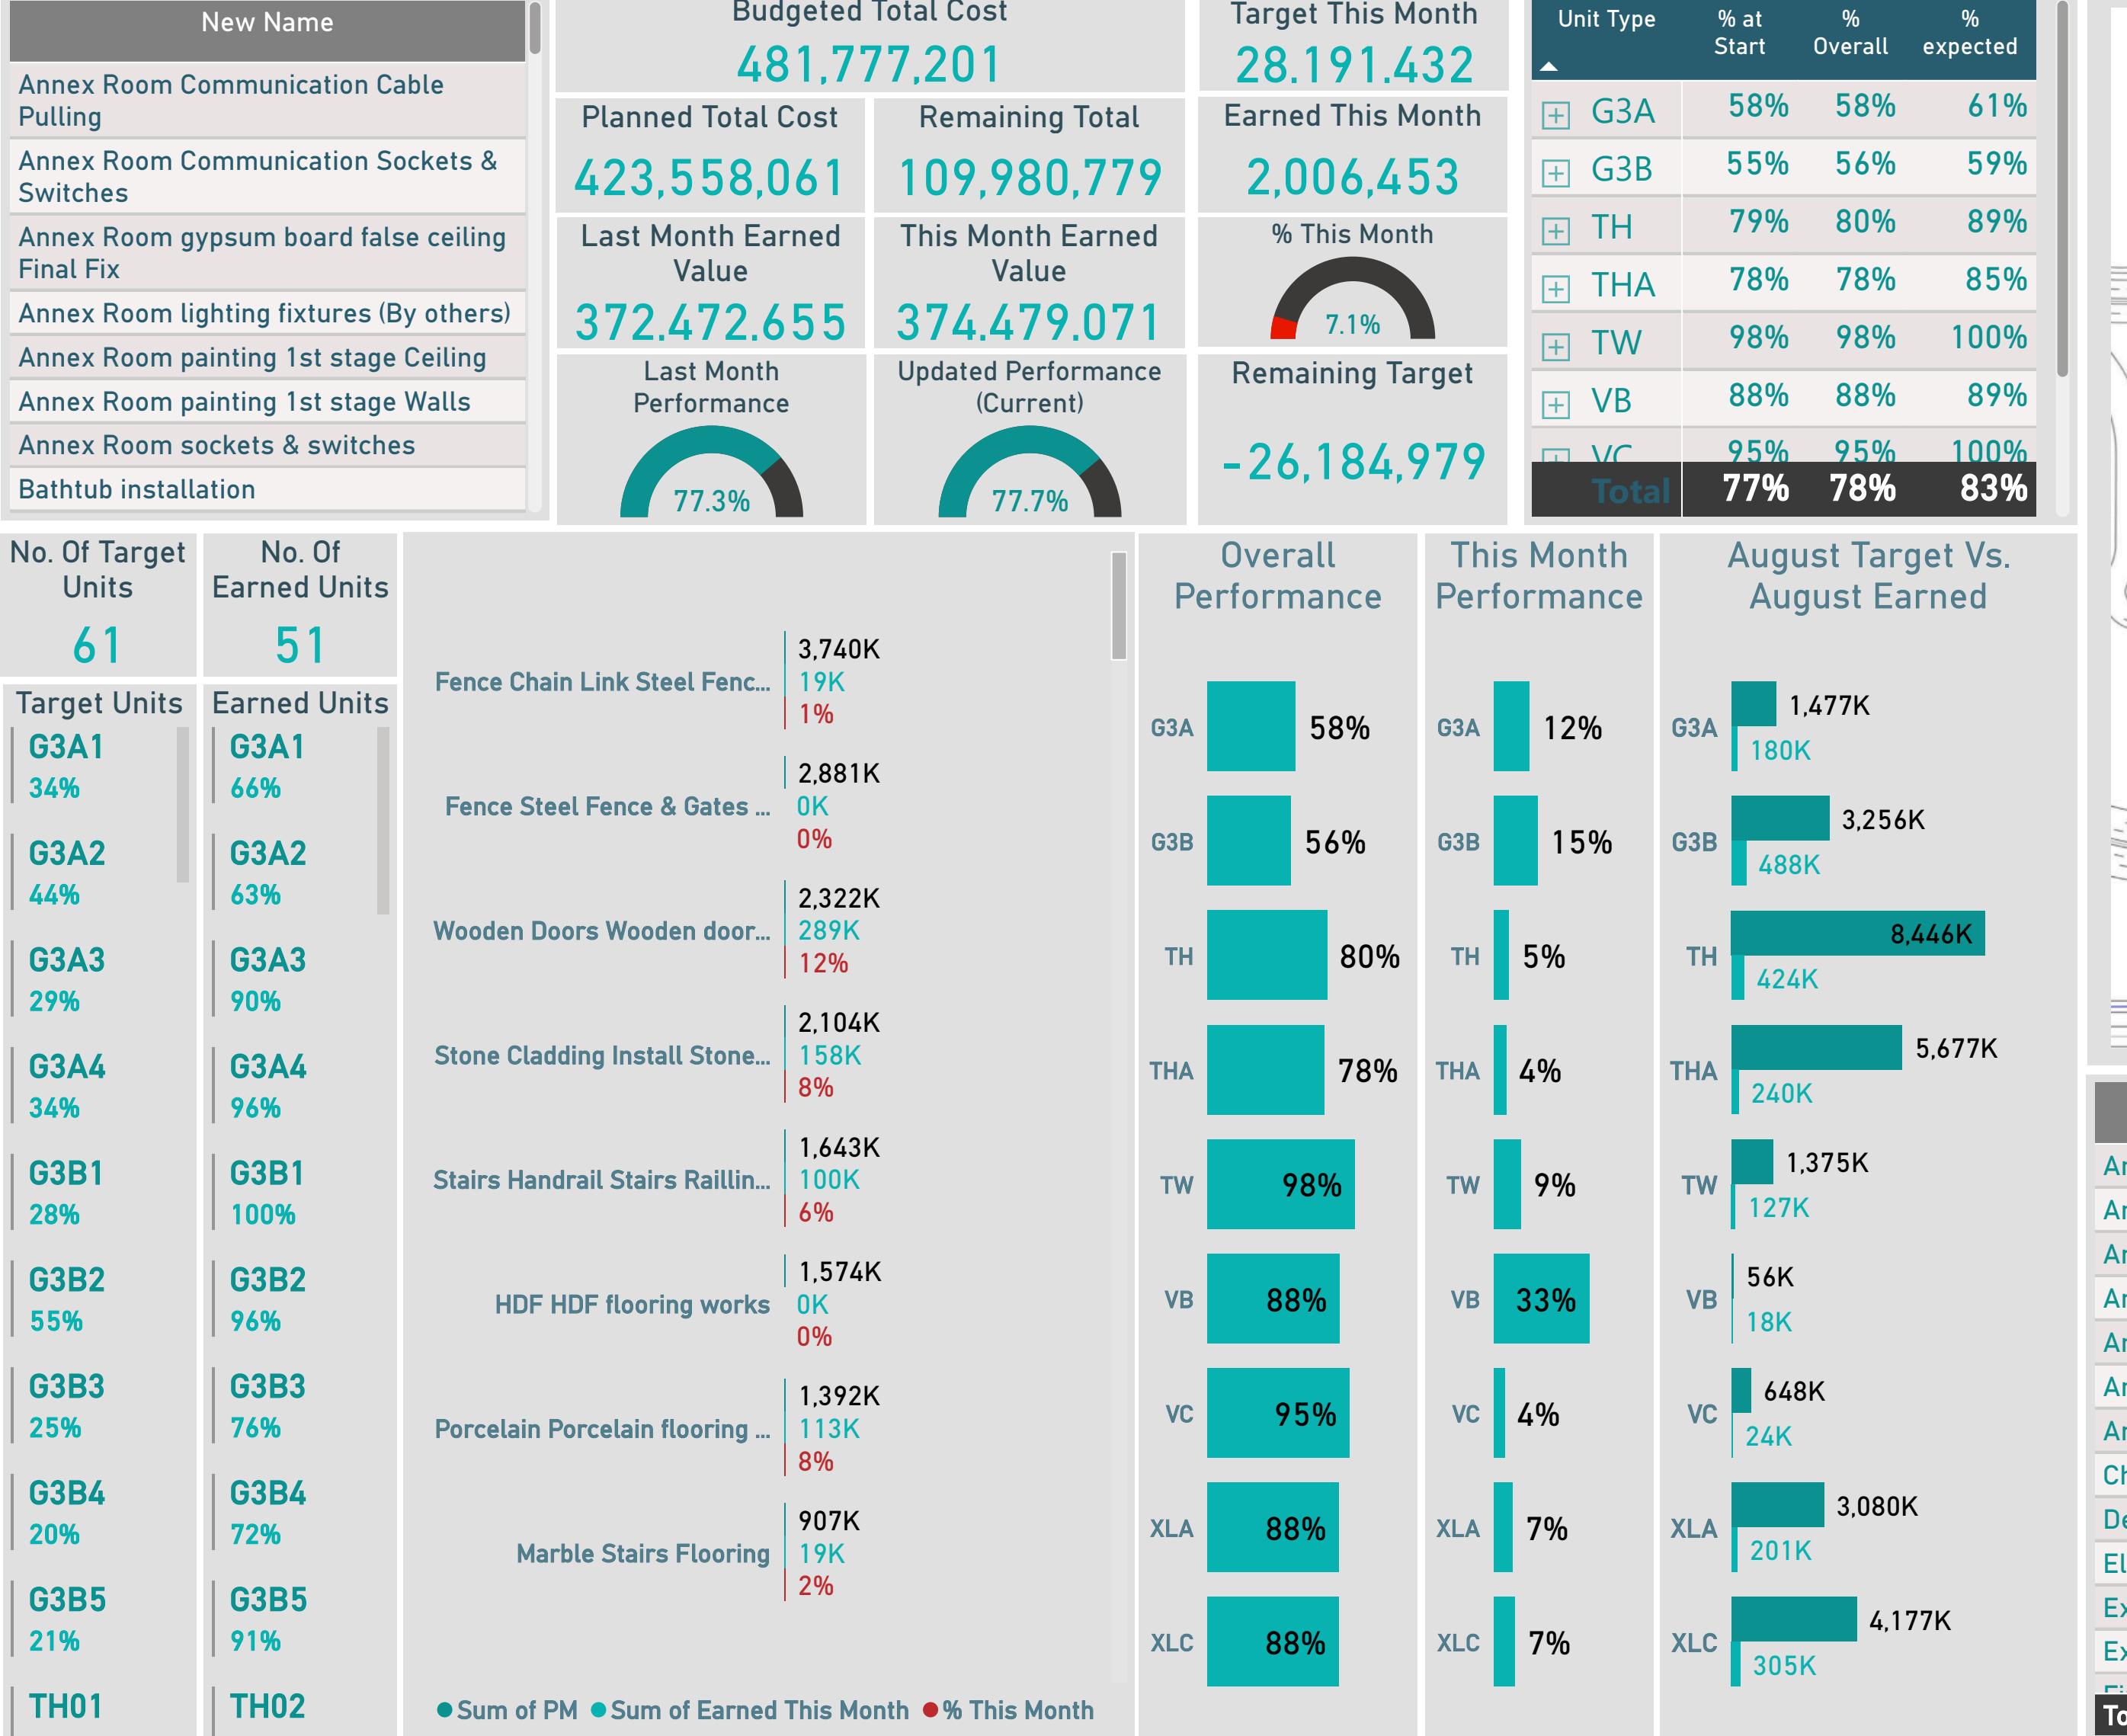

Activity Name	% Start	% Overall	% expected	% Target
Annex Room Communication Cable Pulling	90%	95%	90%	Infinity
Annex Room Communication Sockets and Switches	40%	50%	40%	Infinity
Annex Room gypsum board false ceiling Final Fix	0%	20%	100%	20%
Annex Room lighting fixtures (By others)	40%	50%	40%	Infinity
Annex Room painting 1st stage Ceiling	60%	60%	100%	0%
Annex Room painting 1st stage Walls	60%	60%	100%	0%
Annex Room sockets & switches	40%	50%	40%	Infinity
Chain Link	15%	15%	100%	1%
Decorative Paint	0%	0%	100%	0%
Electrical wiring	95%	98%	95%	Infinity
External PP-R Pipes Installation	0%	0%	100%	0%
External PP-R Pipes Installation for Water Supply	32%	32%	100%	0%
Total	29%	34%	92%	7%

Role
Ahmed Saleh
Bassem Tarek
Mohamed Abd-Mageed
Saleh Kamel
Sub Role
Ahmed Saeed
Ishak
Mostafa Elboray
Tolba
Eslam Mohamed
Hossam Mohamed
Mena Roshdy
Mohamed Ibrahim
Mostafa Diaa
Mohamed Atef
Ghallab Fathi

1/13/2024 2/22/2025

Planning Department Projects Dashboard

ZED EAST



Clear Filters

Select Project

Sawary Phase 02

Shamelbasal Health Unit

Sharona Health Unit

Sherben Hospital

Sidi Heneish

Silver Sand - Land Scape

Silver sands

Solare

Soma Bay Blanca Grand ...

Soma Bay Coves

Whole Sale Market Veget...





Wholesale Market Fish a...

Wholesale Market Infra

Youssef El Sedeek



ZED EAST

ZED Towers - Phase II

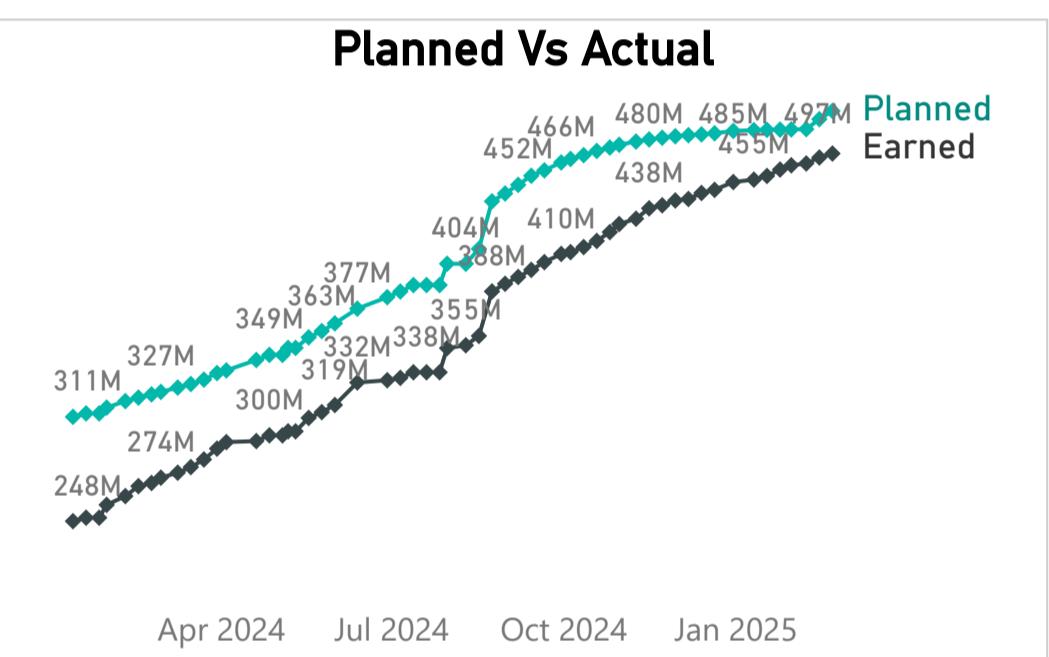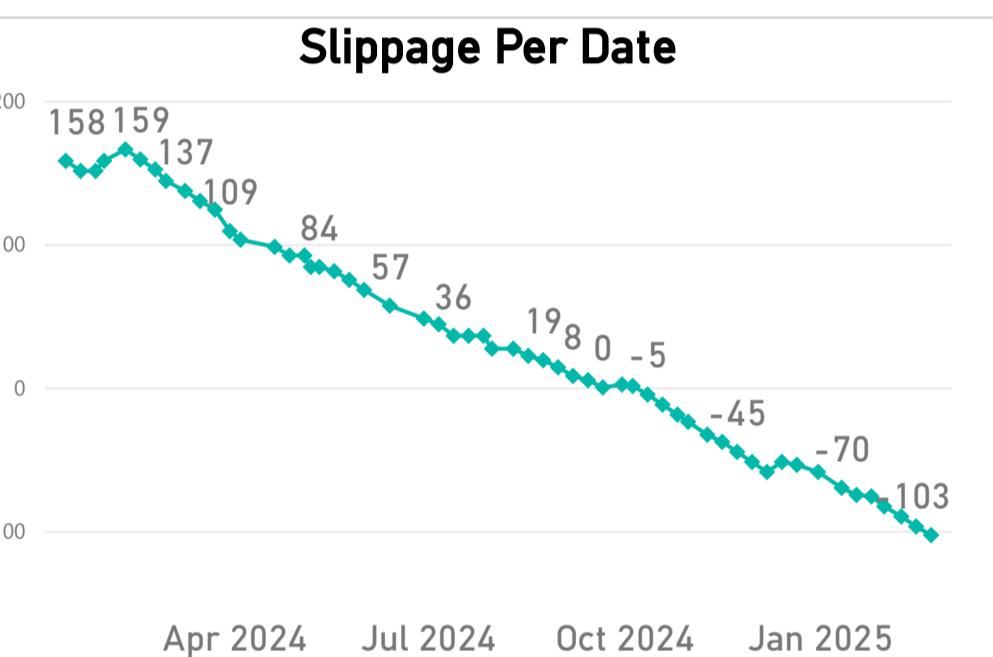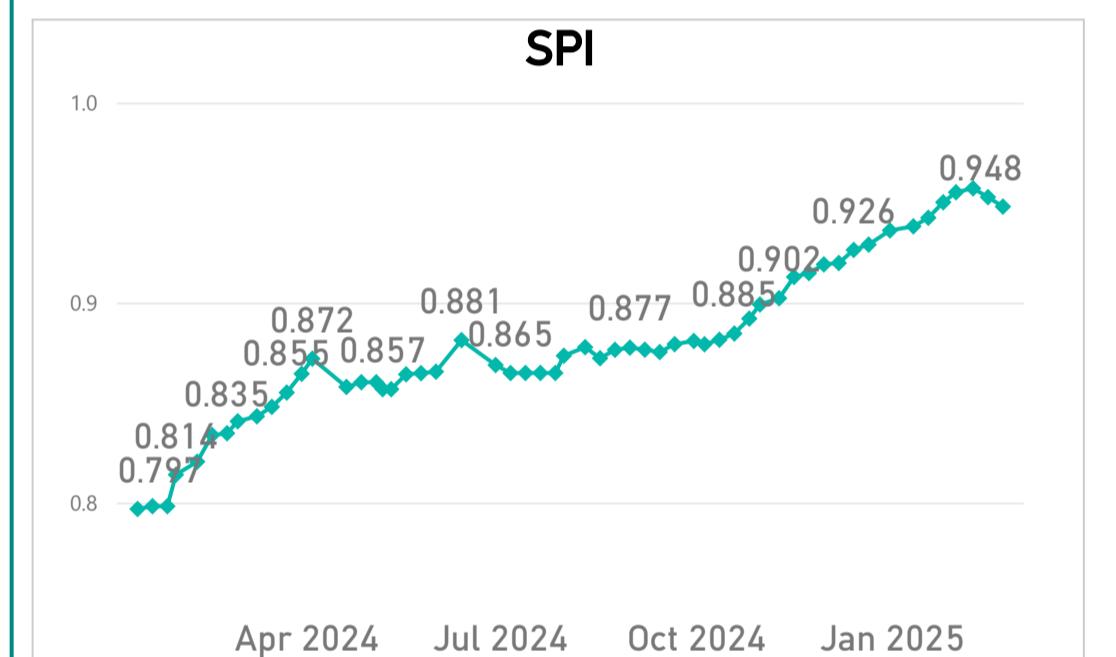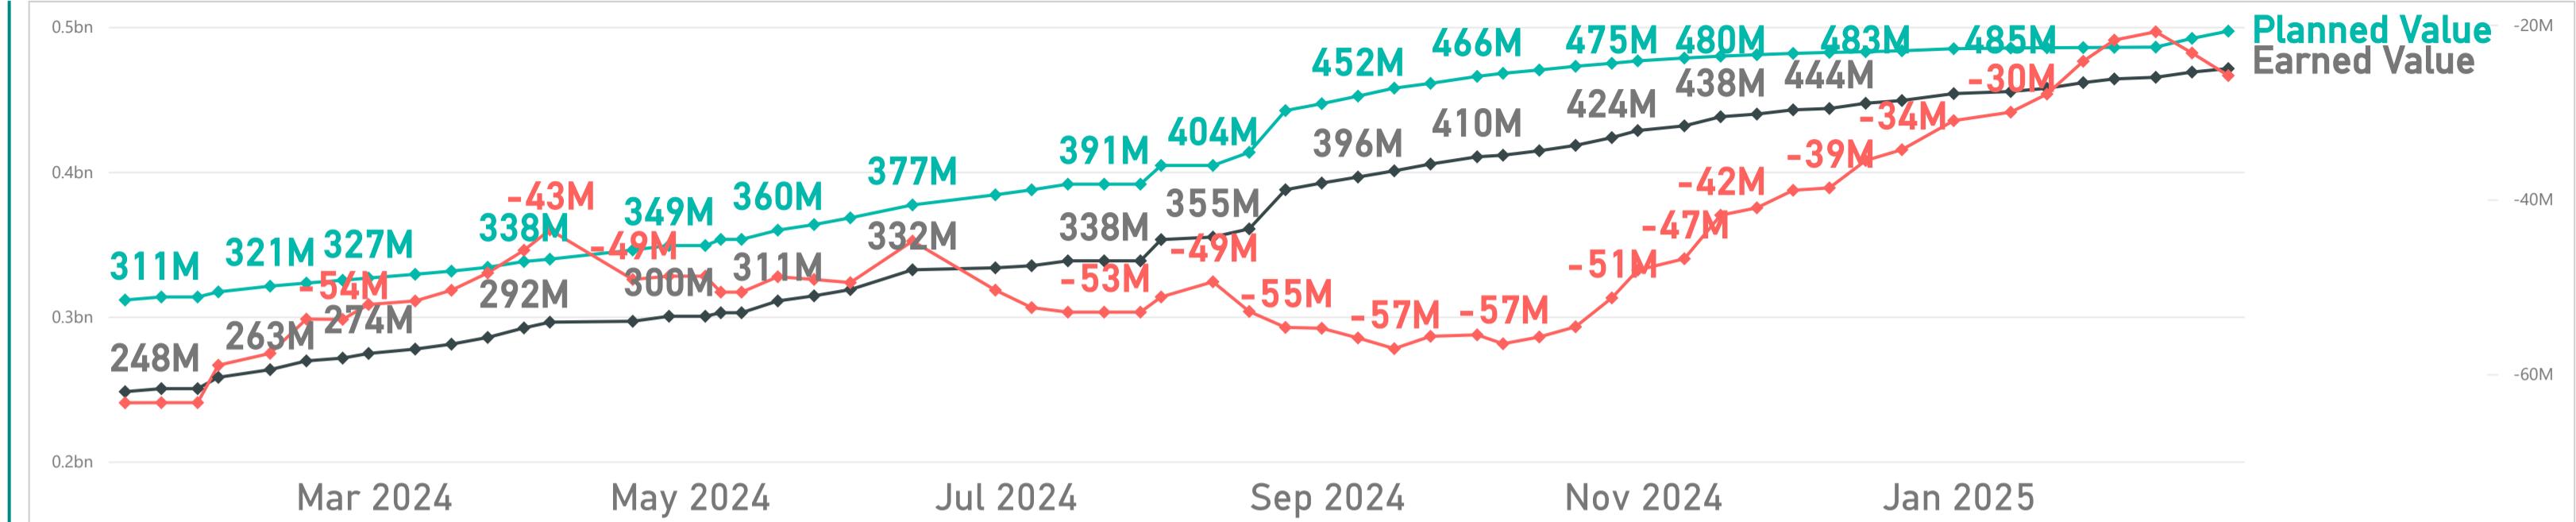


Commencement Date	Contractual Duration
05/09/2022	1013
Contractual Finish Date	Elapsed Days
03/03/2025	901
Expected Finish Date	Remaining Days
14/06/2025	112

Original Contract Value	486,530,662
Earned Value	471,159,229
Planned Value	486,530,662
Month Target	13,018,578
Actual Achieved	6,379,077

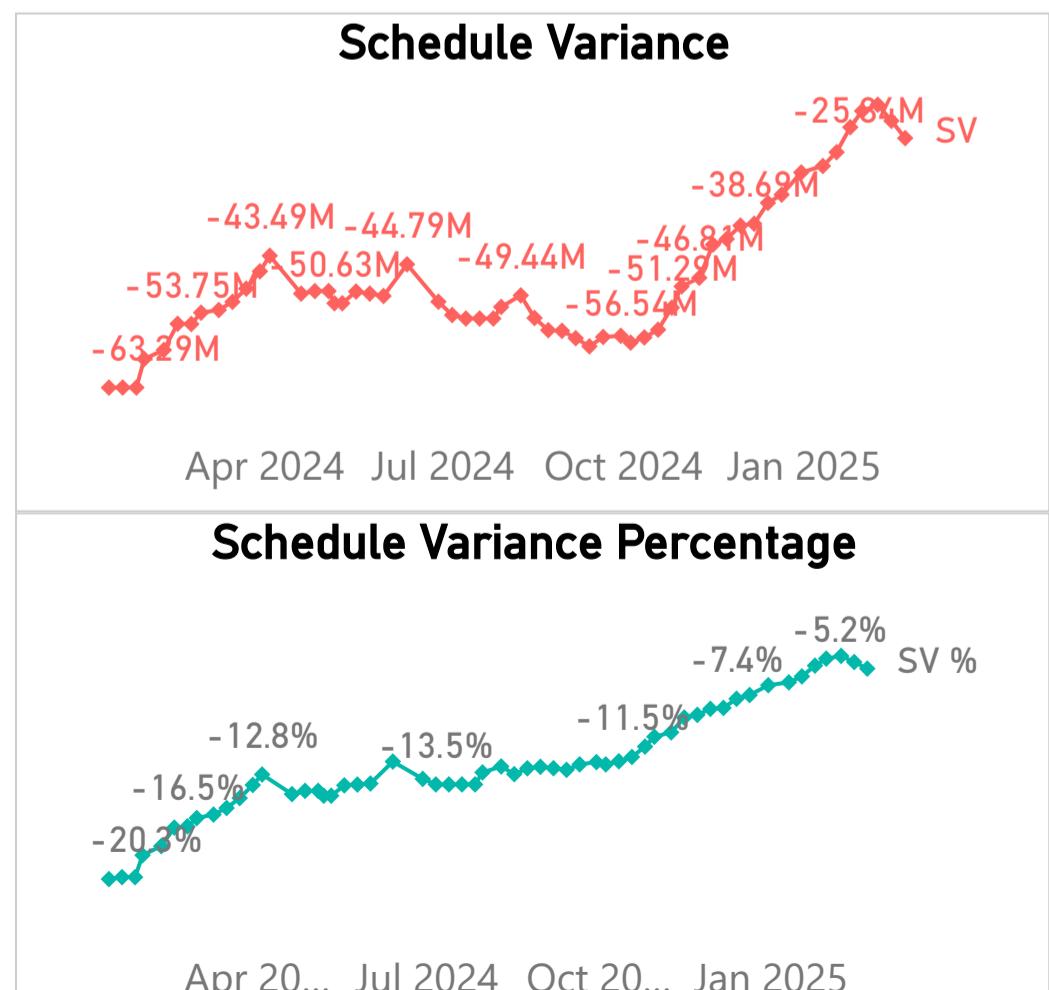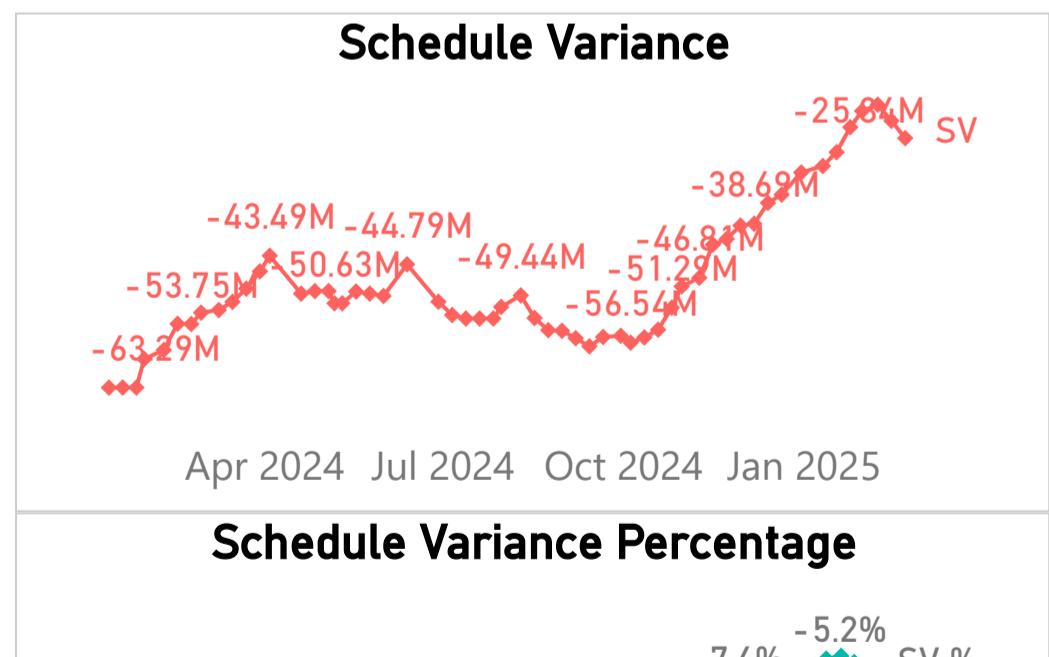

Area Of Concerns		
Data Date	Project Name	Obstacles
22/02/2025	ZED EAST	PM / Planning
22/02/2025	ZED EAST	شركة أولاد أبو المجد (أعمال كريتال السلام و التراسات) - تم رفع المقاسات و لم يتم
22/02/2025	ZED EAST	تقديم جدول زمني لاعمال التوريد و التركيب للعمارات
22/02/2025	Chain Link	لقيادات ZED EAST شركة أولاد أبو المجد (أعمال كريتال) - متبقى تركيب البوابات و
22/02/2025	ZED EAST	المنطقة و الـ Shaft Cover
22/02/2025	ZED EAST	شركة وودك (أبواب خشبية) - مطلوب زيادة اعداد العمالة لانهاء اعمال تسطيب الأبواب
22/02/2025	ZED EAST	في العمارات و Fire Rated للابواب
22/02/2025	ZED EAST	Mطلوب الضغط على مقاولين الخاصة بالتركيبات
22/02/2025	ZED EAST	من الفيلات و العمارات لزيادة اعداد العمالة او توفير بديل لتنشيط ما تبقى .
22/02/2025	ZED EAST	lanهاء اعمال التسطيب و التسلیم (IDG البرنس) مطلوب الضغط على مقاول الرخام للفيلات
22/02/2025	ZED EAST	لأسنیرات العمارات مطلوب سرعة توريد الـ Horn & Speakers
22/02/2025	ZED EAST	للعمارات من شركة إيلاف مطلوب سرعة توريد باقي اكسسوارات Wiring Devices
22/02/2025	ZED EAST	مطلوب سرعة توريد باقي كمية السيراميك المطلوبة للعمارات
22/02/2025	ZED EAST	مطلوب سرعة توريد طلب الشراء الخاص بالـ Sanitary Fixtures Fitting
22/02/2025	ZED EAST	مطلوب سرعة توريد لوحات العدادات للعمارات

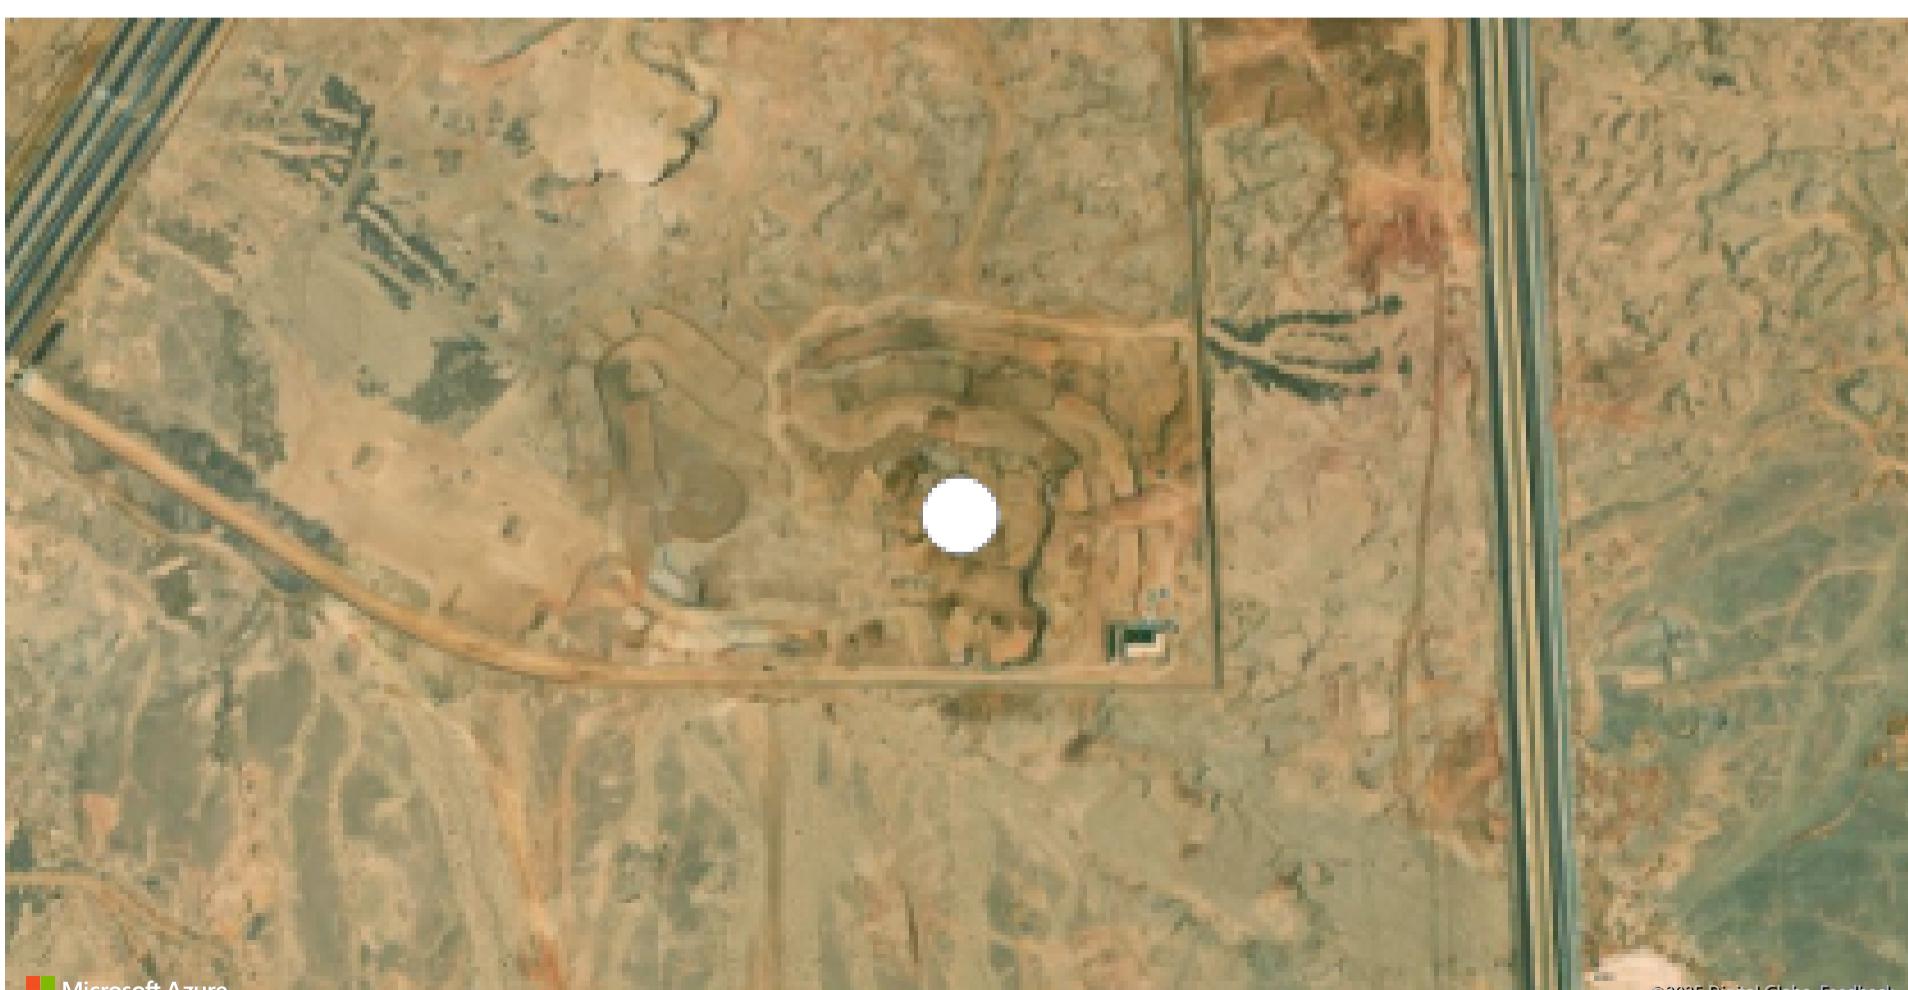



Shop Drawing Status



REDCON
CONSTRUCTION
genuinely green


Last Submitted Date

4 August, 2024

Last Approval Date

31 July, 2024


Count by Status

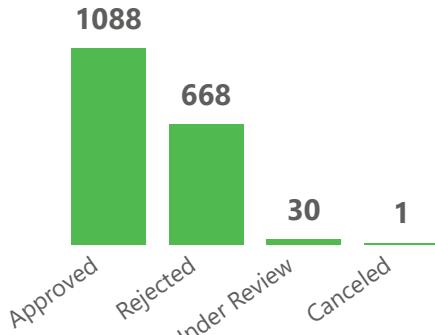

Count by Unit Type

TW	443
G3	211
THR	205
THA	204
VXC	188
VXA	185
VC	179
VB	126
General	37
TH	1
TW&VB	1
TW&VC	1
TW24	1
TW25	1

KPI




Total

1,787


Approved

1,088

Count by Rev. No.




Count by Duration Status



Count by Unit Type

CIVIL	555
ARCH	517
Mechanical	407
Electrical	308

Approved by Rev.






RFI Status




REDCON
CONSTRUCTION
genuinely green


Count by Status

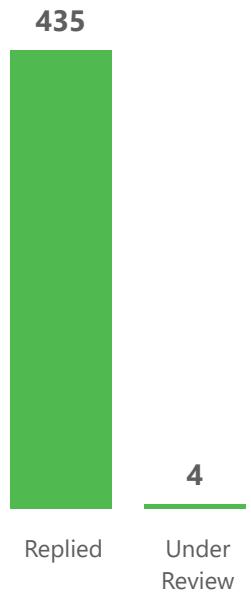


Count by Unit Type

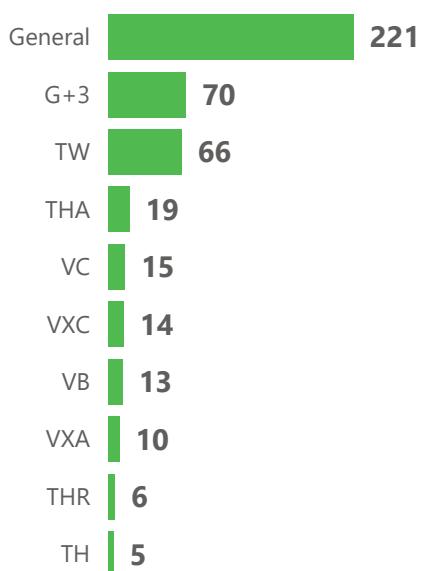


Count by Discipline

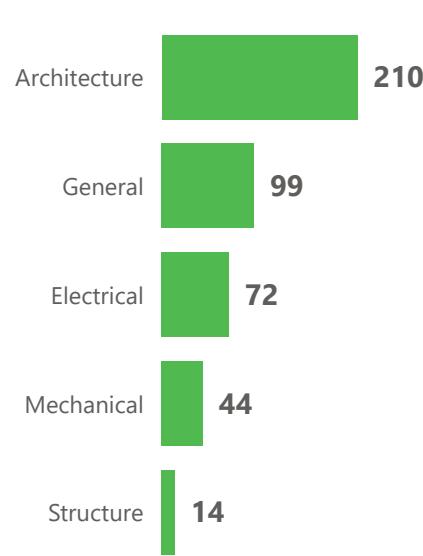

Count by Duration Status



Count by Rev. No.

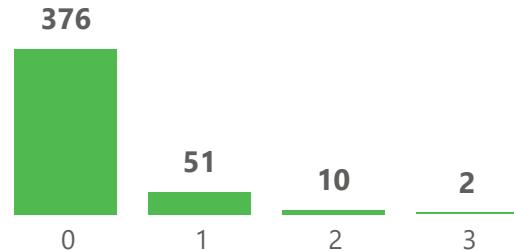










MAR Status



REDCON
CONSTRUCTION
genuinely green

Last Submitted Date
3 August, 2024

Last Replied Date
4 August, 2024

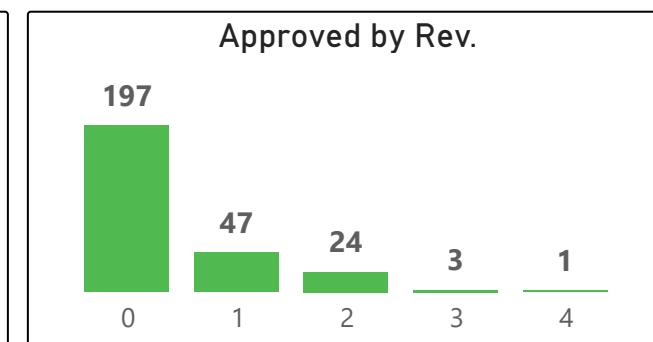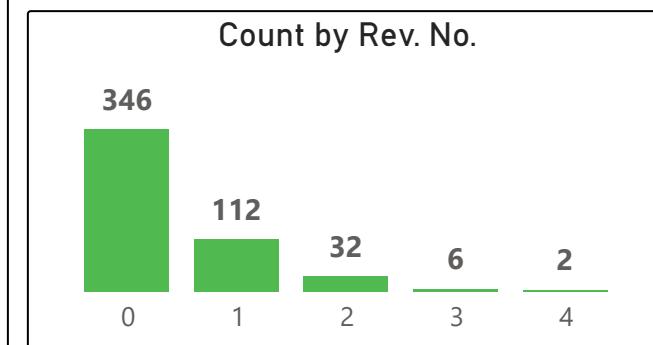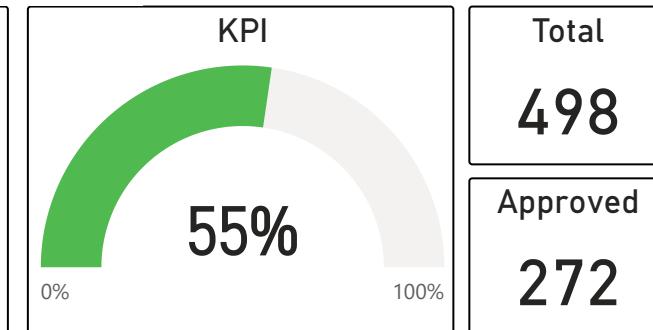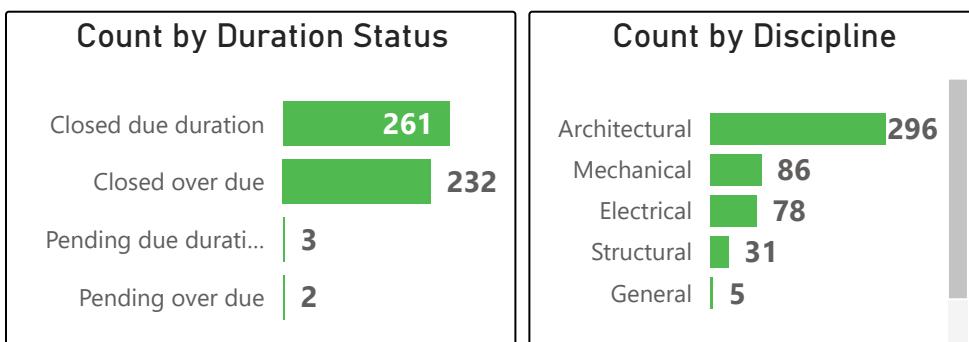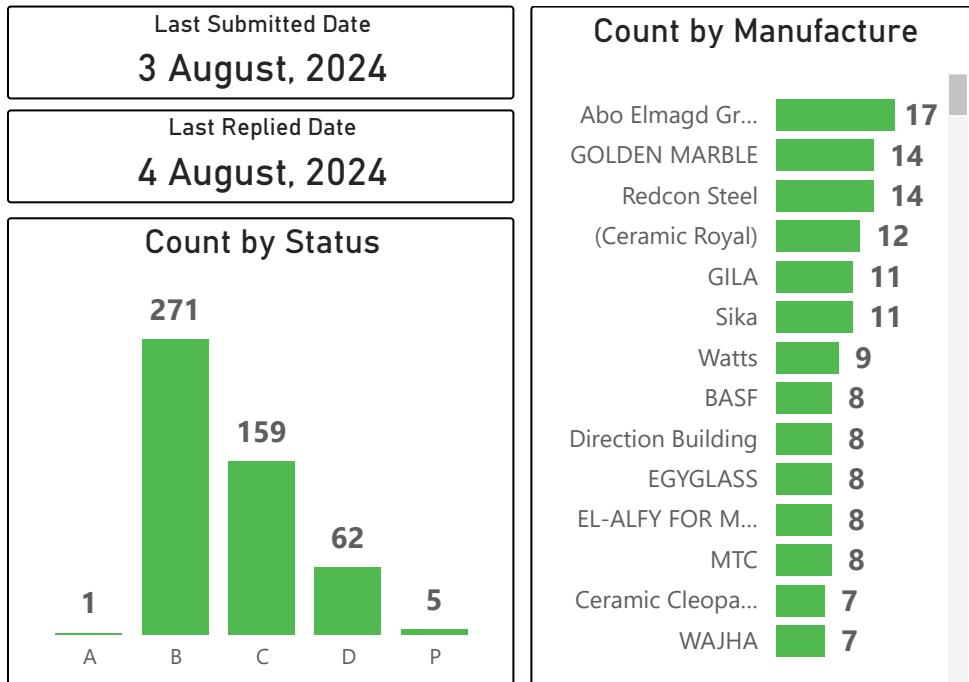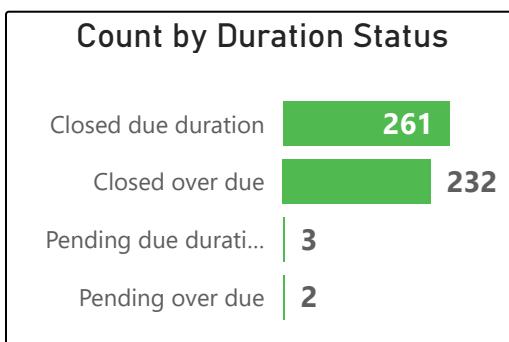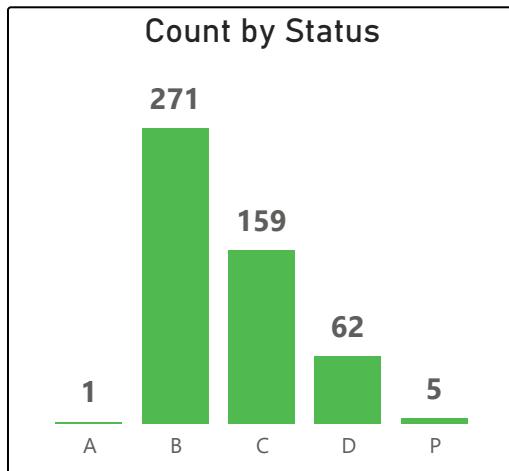



Zed East - Package A - RCN

Weekly Dashboard



Clear Filters



Unit Type	G3A	TH	TW	VC	XLC
	G3B	THA	VB	XLA	

Unit Number				
G3A1	TH02	THA12	TW12	TW29
G3A2	TH03	THA13	TW16	TW30
G3A3	TH04	THA14	TW17	TW31
G3A4	TH05	THA15	TW18	TW33
G3B1	TH06	THA16	TW19	TW34
G3B2	Th07	THA17	TW21	TW35
G3B3	TH08	TW01	TW24	VB12
G3B4	TH09	TW04	TW25	VC27
G3B5	THA10	TW05	TW26	VC28
TH01	THA11	TW10	TW28	VC29

Level	1st	3rd	FCD	GR	SOGL
	2nd	4th	FOL	RF	

Items Description

- Concrete insulation works
- Concrete works
- Electrical works
- Engineering Wood
- Fencing






- External plastering works
- Façade quarry tiles cladding
- False ceiling works
- Glass Handrail
- HDF
- Hvac works
- Internal painting works
- Internal plastering works
- Marble & granite flooring
- Masonry works
-

Activity Name ▼

400 micron polyethylene sheet under Sl...

- Annex Room Communication Cable Pulling
- Annex Room Communication outlets cond...
- Annex Room Communication Sockets & S...
- Annex Room gypsum board false ceiling ...

	Planned	Actual	%
Annex Room install UPVC pipes for AC	100%		
Annex Room lighting fixtures (By others)	100%		
Annex Room masonry works	100%		
Annex Room painting 1st stage Ceiling	100%		
Annex Room painting 1st stage Walls	100%		
Annex Room painting final coat	100%		
Annex Room plastering works 1st stage	100%		
Annex Room plastering works final stage	100%		
Annex Room Refrigerant Pipes Installation	100%		
Annex Room sockets & switches	100%		

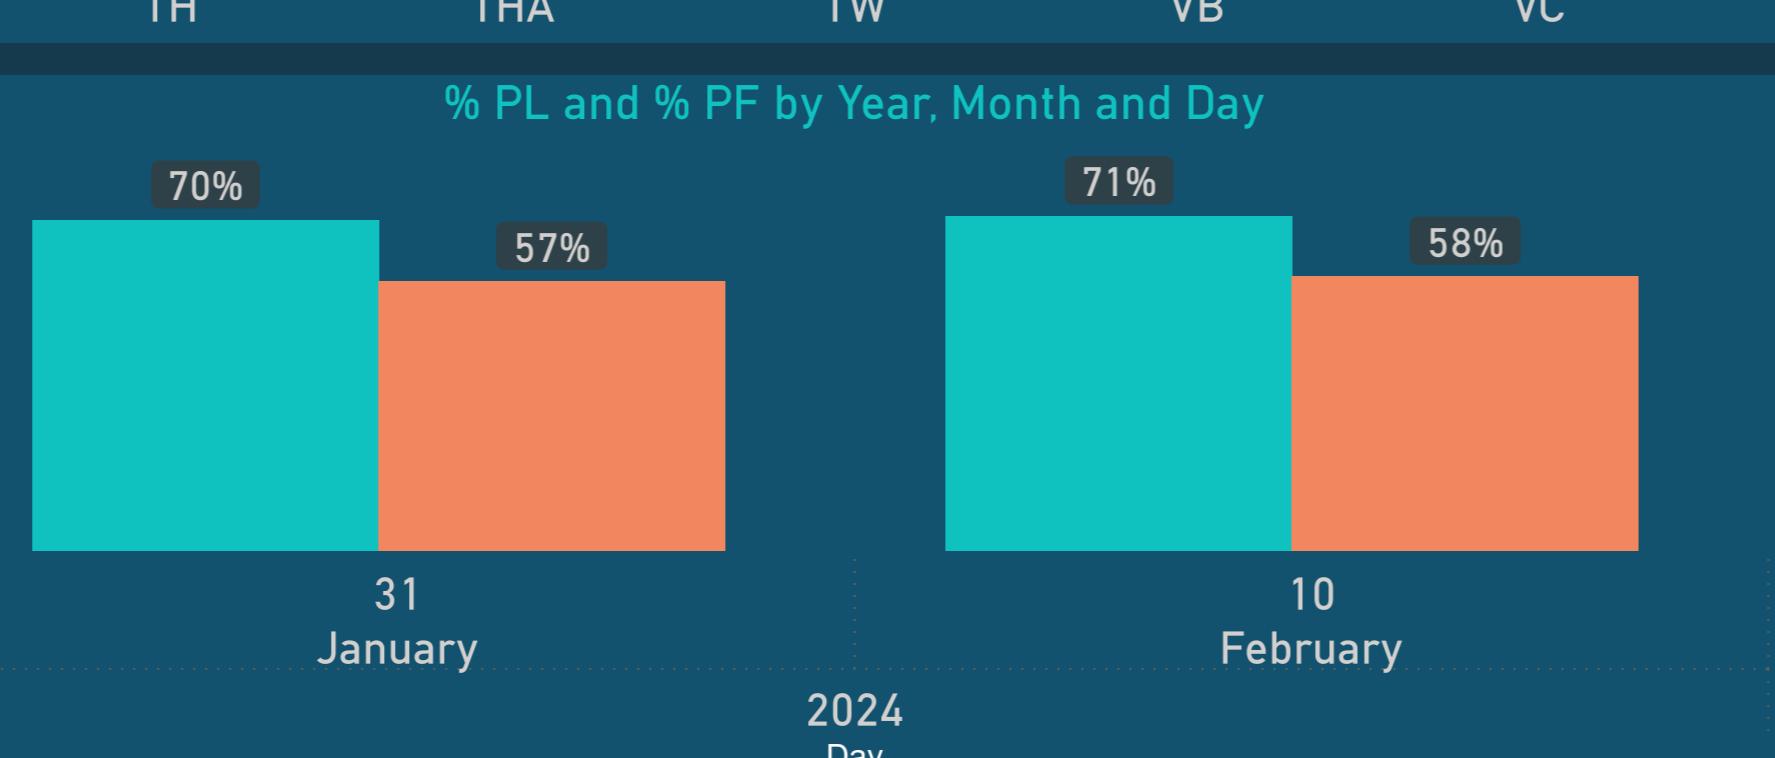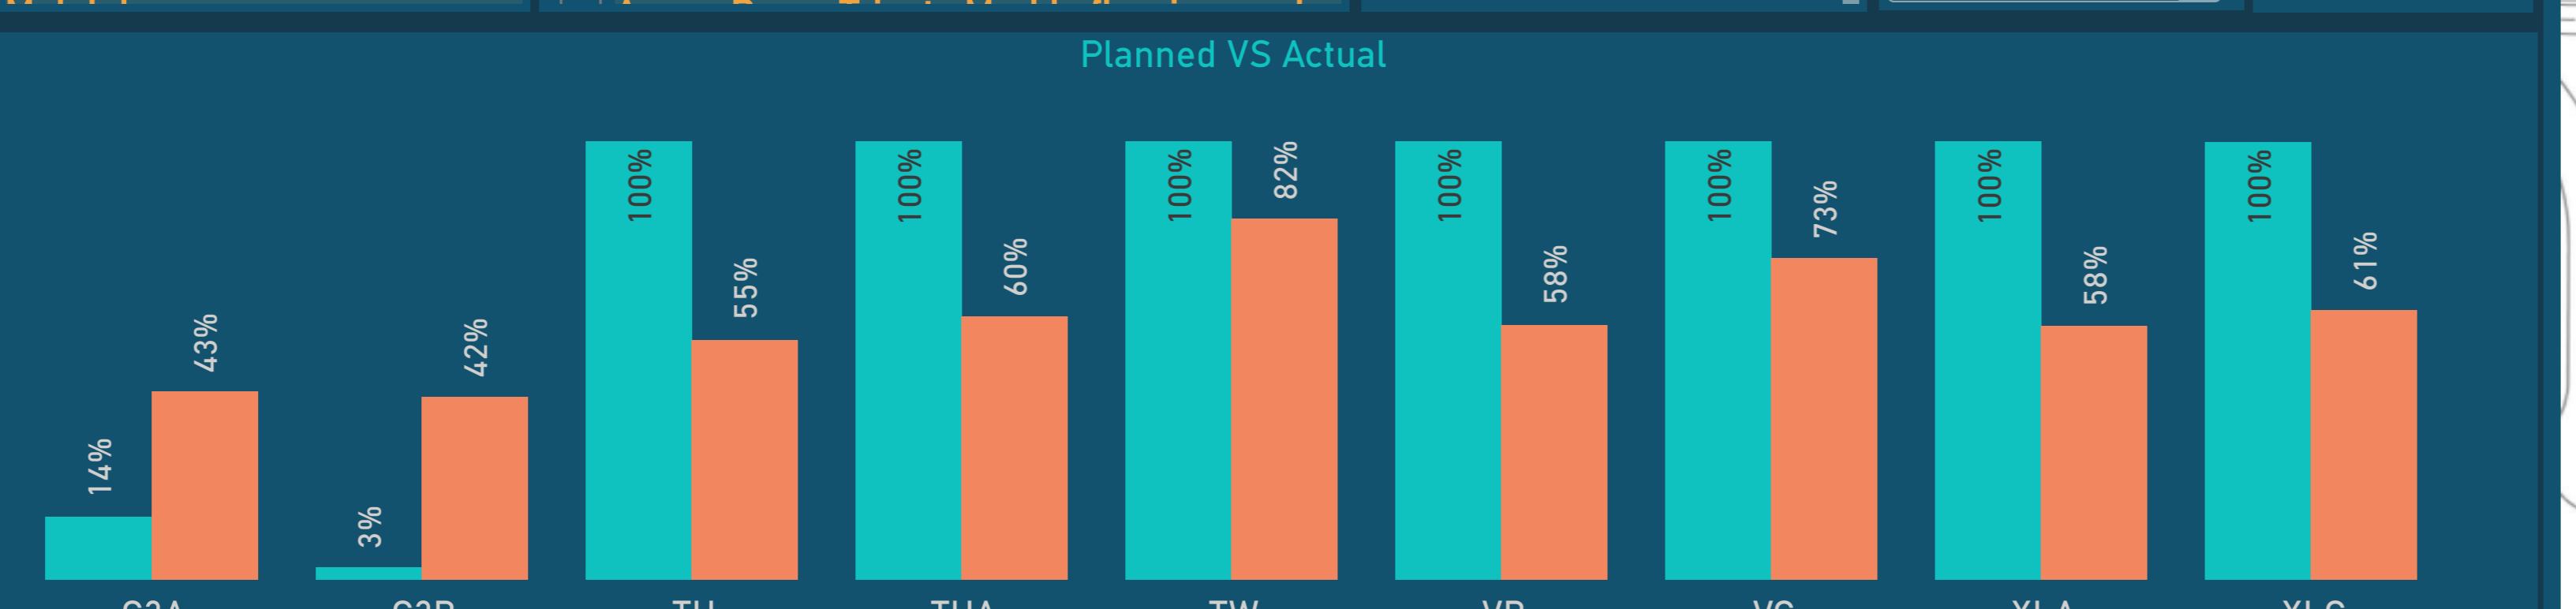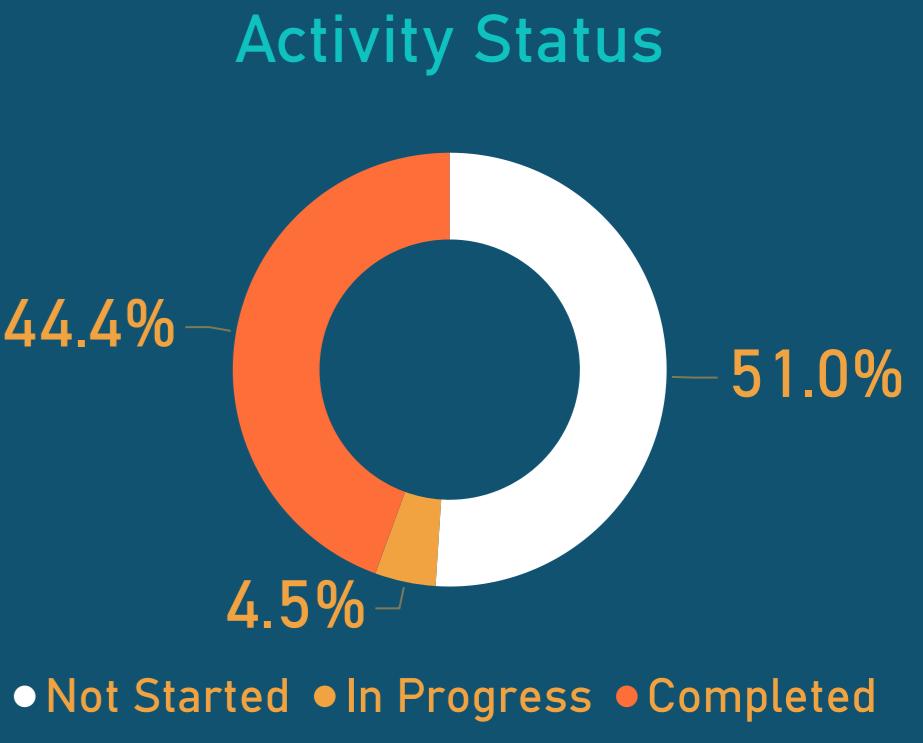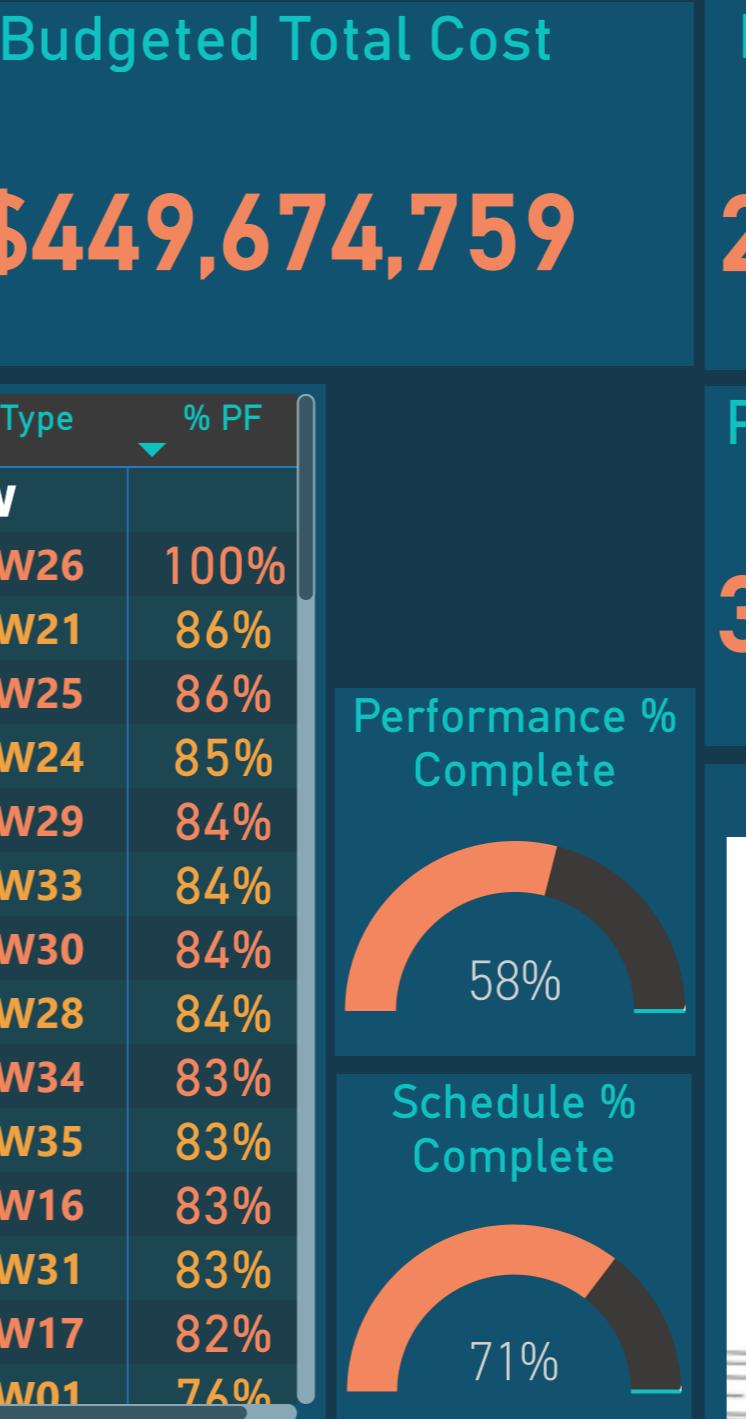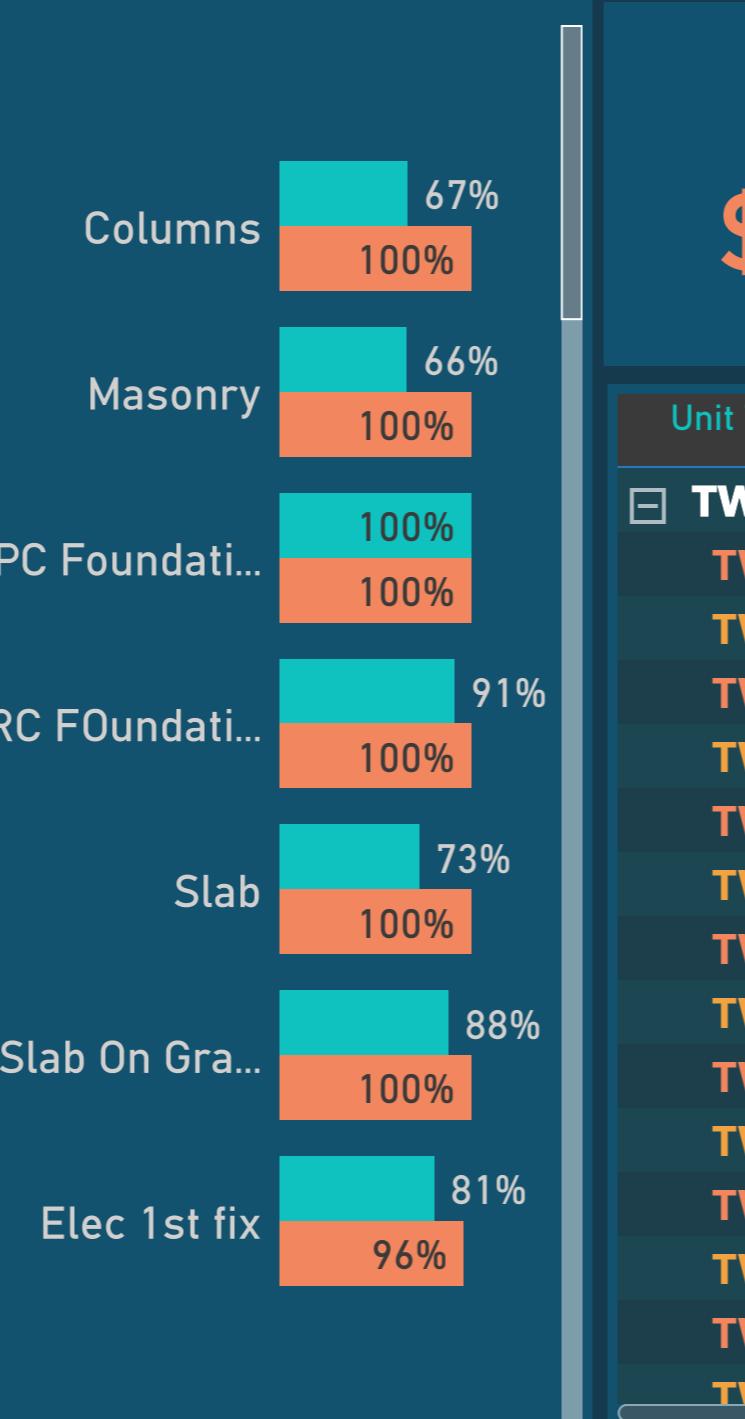



Sections
Buldings | **Villas**

Unit Type
G3A | **G3B** | **TH** | **THA** | **TW** | **VB** | **VC** | **XLA** | **XLC**

Unit Number
All




Items
All

Discipli...
All


Level
All

Work Package	
<input type="checkbox"/>	Cables & Wires
<input type="checkbox"/>	Ceramics
<input type="checkbox"/>	Columns
<input type="checkbox"/>	Earthing systems
<input type="checkbox"/>	Elec 1st fix
<input type="checkbox"/>	Equipment Cabinet IEC
<input type="checkbox"/>	External Painting
<input type="checkbox"/>	External Plaster
<input type="checkbox"/>	Floor Distribution Boards
<input type="checkbox"/>	Floor Drains
<input type="checkbox"/>	Gypsum Board
<input type="checkbox"/>	HDF
<input type="checkbox"/>	HVAC
<input type="checkbox"/>	Inspection Chambers & Hos...
<input type="checkbox"/>	Internal Painting
<input type="checkbox"/>	Internal Pipes
<input type="checkbox"/>	Internal Plaster
<input type="checkbox"/>	Lighting Fixtures
<input type="checkbox"/>	Marble
<input type="checkbox"/>	Masonry
<input type="checkbox"/>	Panel Boards
<input type="checkbox"/>	PC Cement Screed
<input type="checkbox"/>	PC Foundation
<input type="checkbox"/>	Porcelain
<input type="checkbox"/>	RC Foundation
<input type="checkbox"/>	RC Insulation
<input type="checkbox"/>	Risers
<input type="checkbox"/>	Roof Aggregate
<input type="checkbox"/>	Roof Drains
<input type="checkbox"/>	Roof Metal Flashing
<input type="checkbox"/>	Roof Water Proofing
<input type="checkbox"/>	Sanitary Fixtures
<input type="checkbox"/>	Slab
<input type="checkbox"/>	Slab On Grade
<input type="checkbox"/>	Stairs Handrail
<input type="checkbox"/>	Steel Ladder Hook
<input type="checkbox"/>	Stone Cladding

New Name	
400 micron polyethylene sheet under Slab on Grade	
Annex Cable Pulling	
Annex Room Communication outlets conduits installation	
Annex Room gypsum board false ceiling 1st Fix	
Annex Room install UPVC pipes for AC	
Annex Room masonry works	
Annex Room painting 1st stage Ceiling	
Annex Room painting 1st stage Walls	
Annex Room plastering works 1st stage	

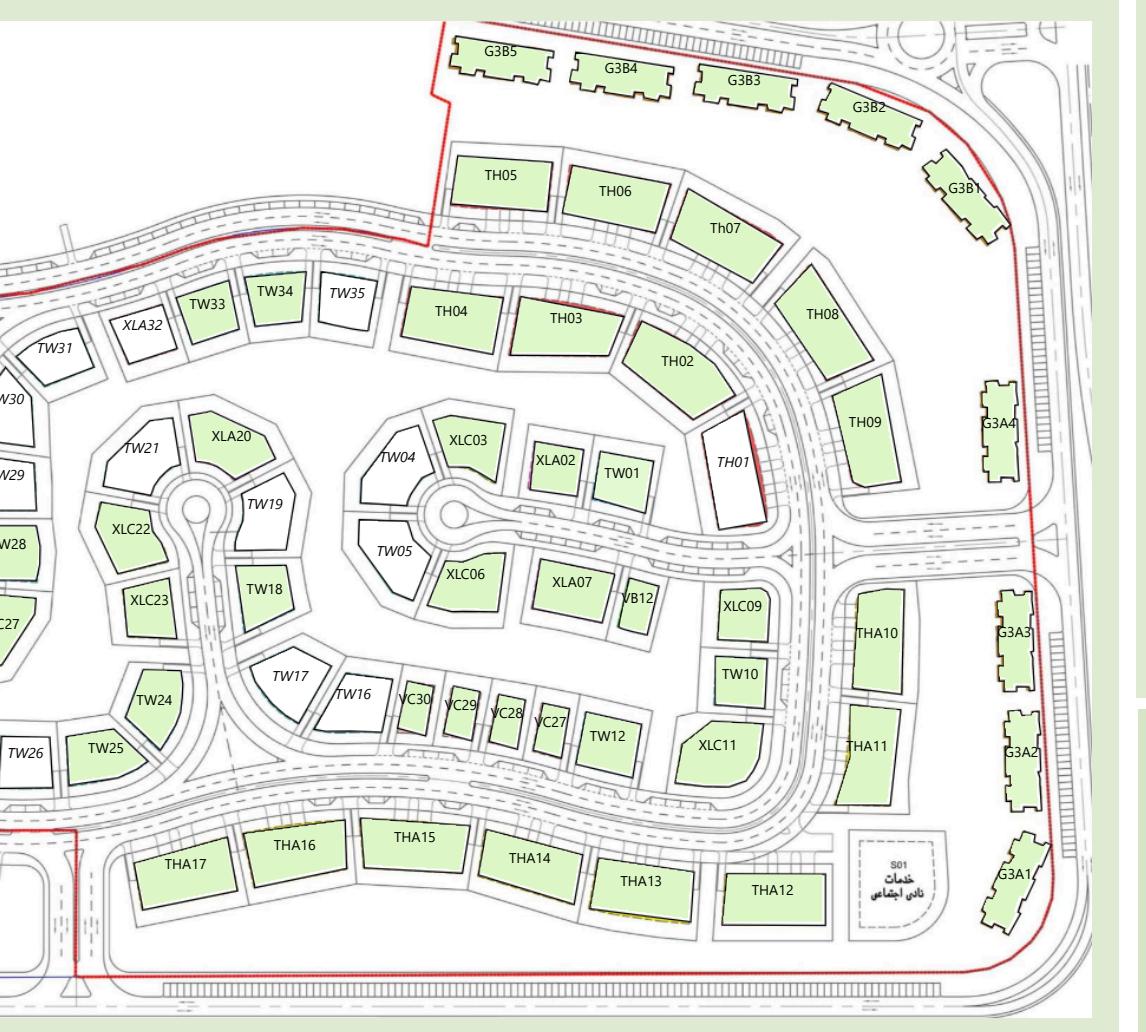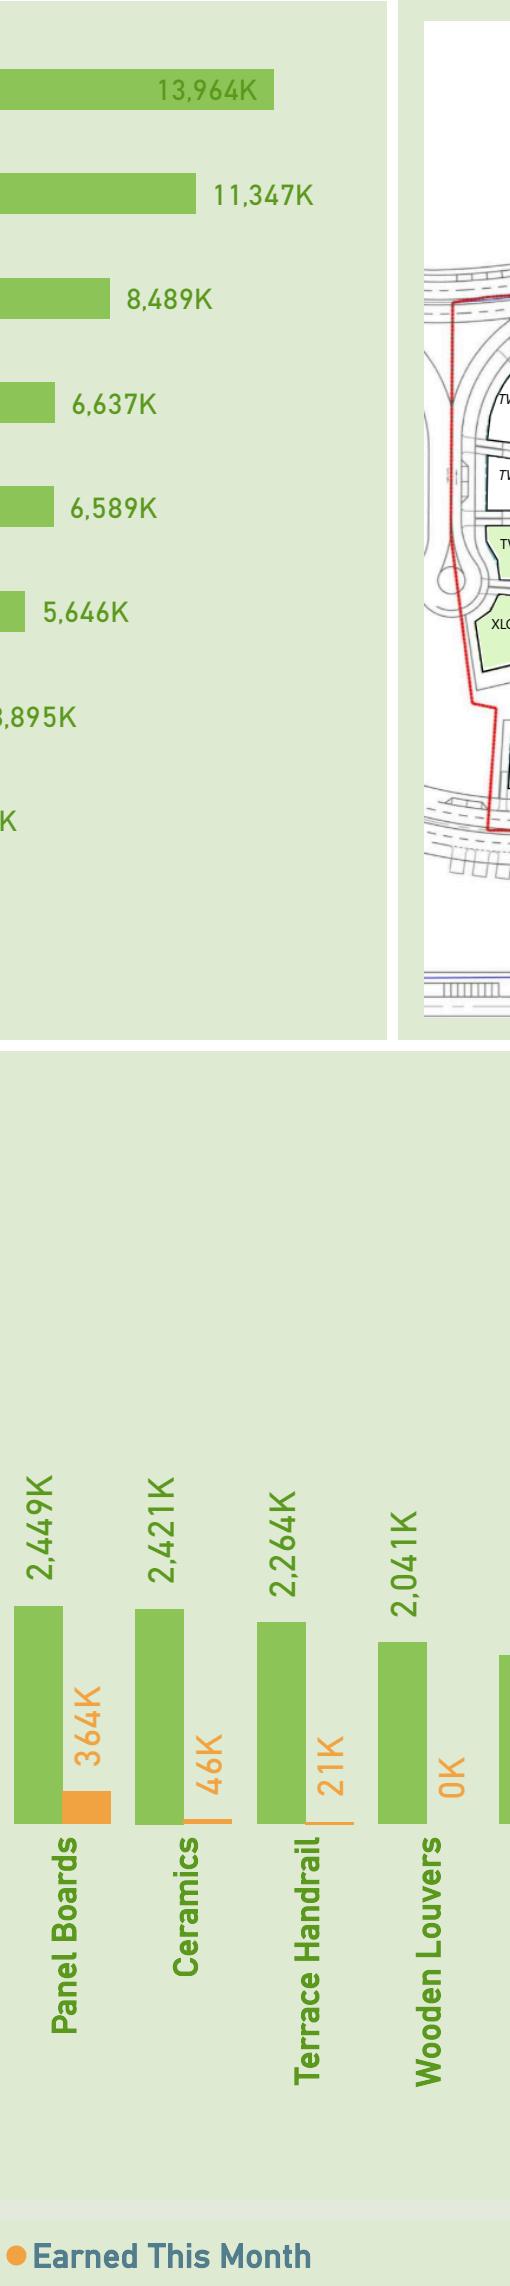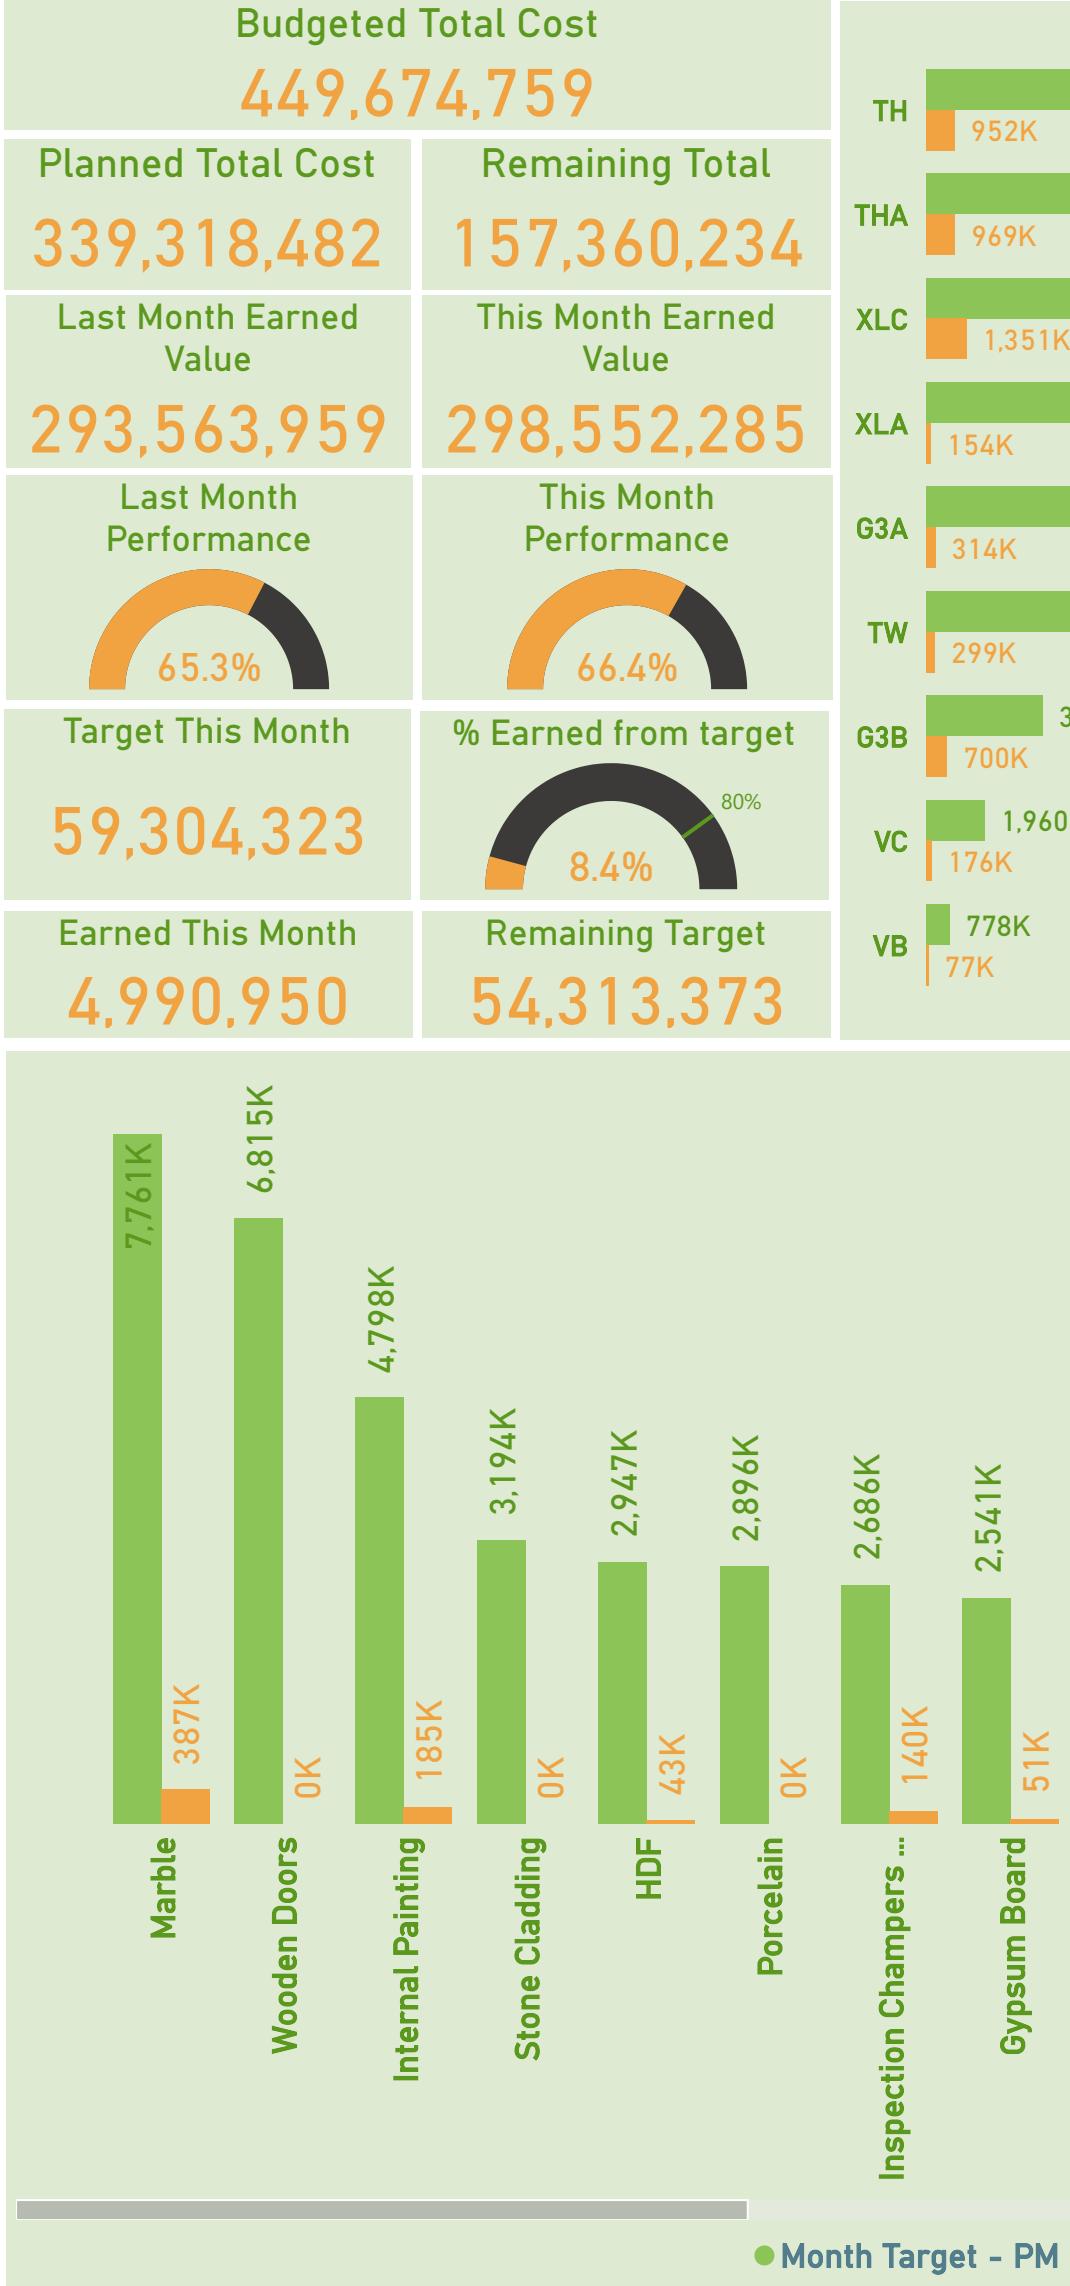


Unit Type	% Schedu...	Old perfor...	New perfor...	Remaining Target	New Remaining
G3A	38%	46%	46.05%	6,274,901	34,254,491
G3B	11%	45%	45.66%	3,194,529	43,195,768
TH	100%	68%	69.46%	13,012,188	22,831,601
THA	100%	66%	67.44%	10,378,468	24,509,603
TW	100%	91%	91.44%	5,347,163	7,215,030
VB	100%	65%	66.95%	700,881	1,053,325
VC	100%	80%	81.25%	1,783,497	2,183,943
XLA	100%	68%	68.90%	6,483,422	7,016,943
XLC	100%	71%	74.73%	7,138,324	8,861,770
Total	75%	65%	66.39%	54,313,373	151,122,474

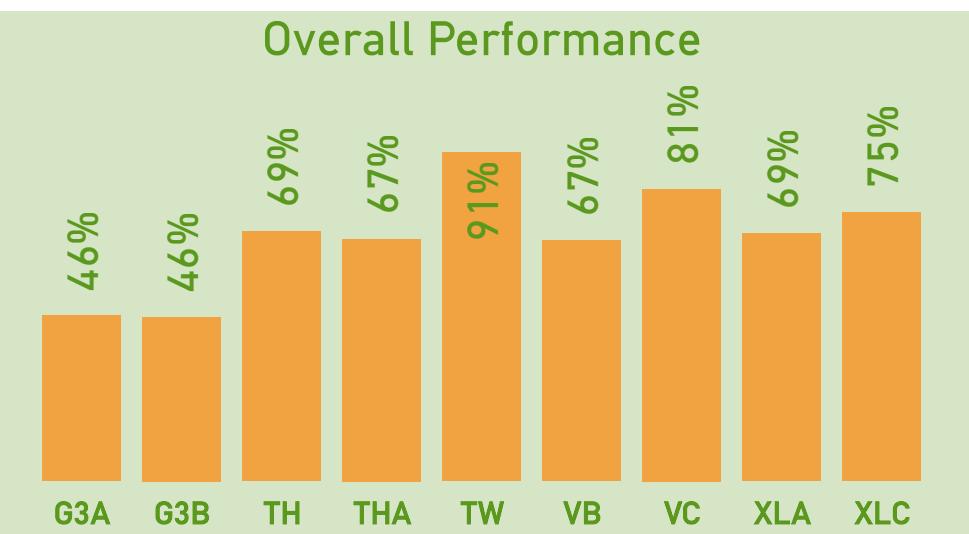


Activity Name
Annex Room gypsum board false ceiling 1st Fix
Annex Room painting 1st stage Ceiling
Annex Room painting 1st stage Walls
Annex Room Triesta Marble flooring works
External Painting Works (Render/Acrylic Paint)
External PP-R Pipes Installation
External PP-R Pipes Installation for water supply
Final Touch Up
First floor Stone Vanity and Stone Counter Tops Installation for wet areas
First floor Stone Vanity Top Installation for wet areas
First floor 2mm thick cementious waterproofing for wet areas-Duplex 1
First floor Bathtub installation
First Floor Cables
First floor Cement Tiles works under HDF Flooring
First floor Cement Water Proofing for wet areas
First floor Communication Cable pulling

● Month Target - PM ● Earned This Month

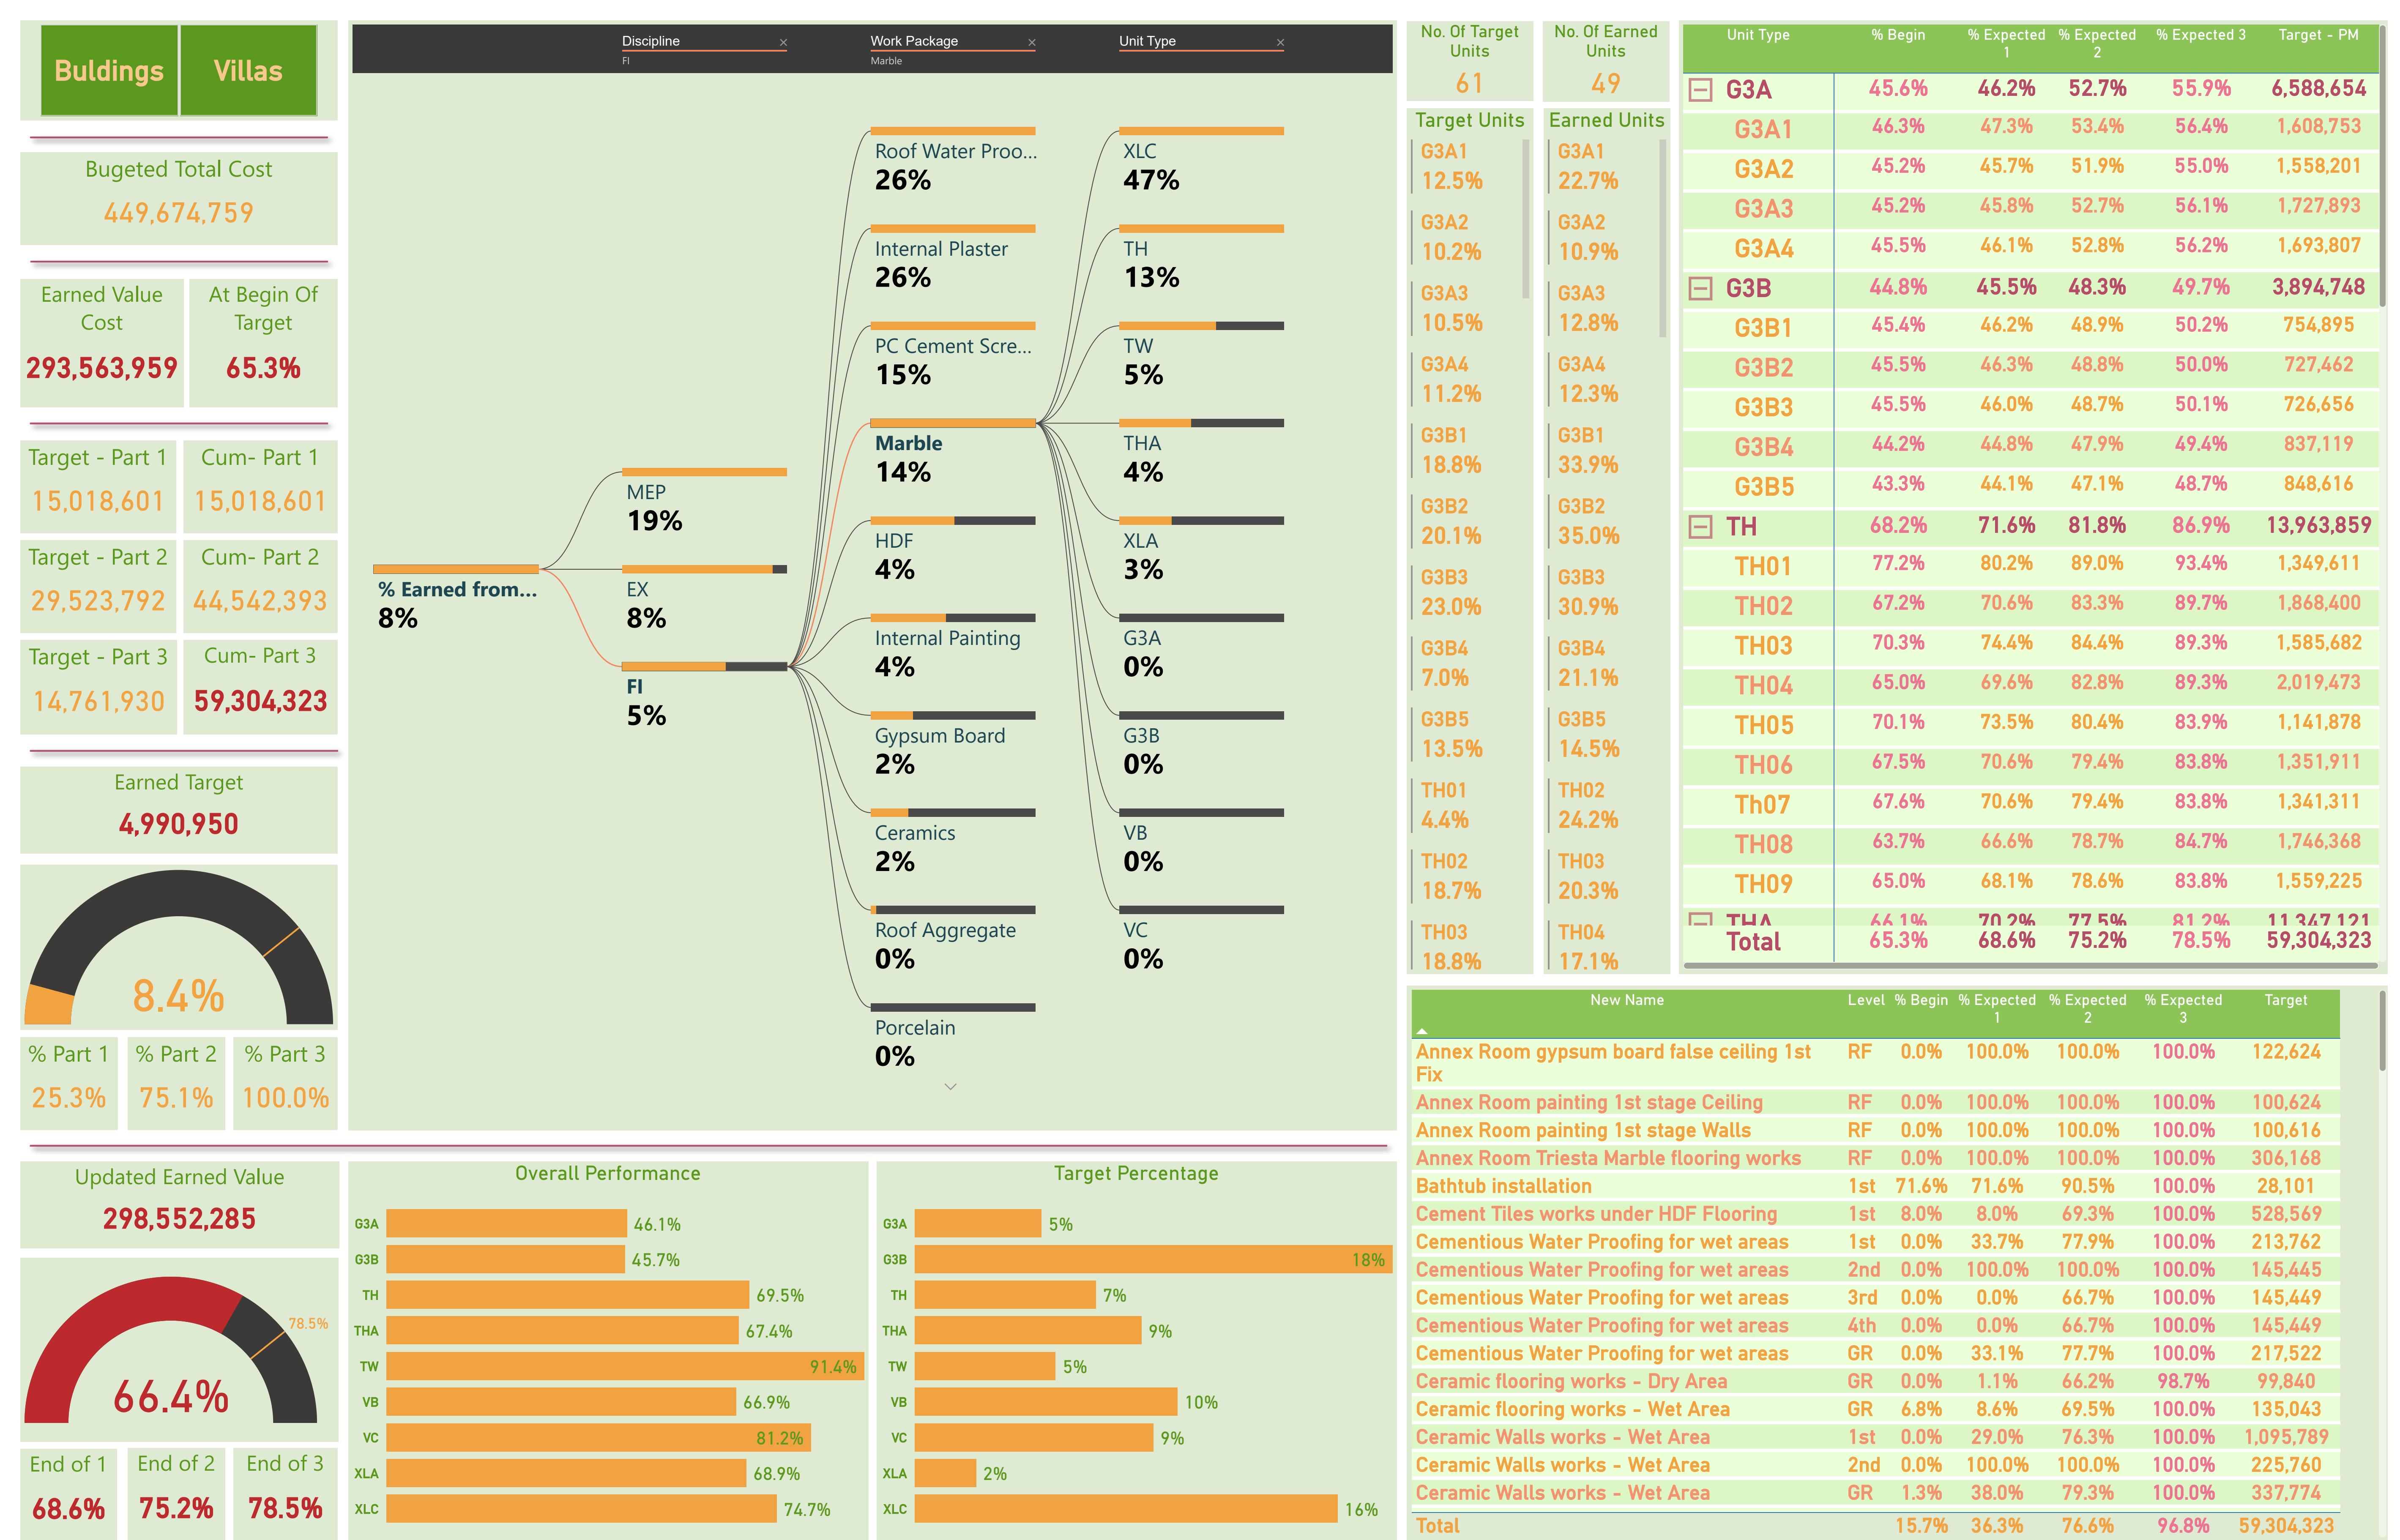

**Data Date :
Saturday, October 26, 2024**

Unit Type	TH	THA	TW	VB	VC	XLA	XLC
Location	Fence	Villas					
Discipline	Finishes	MEP					

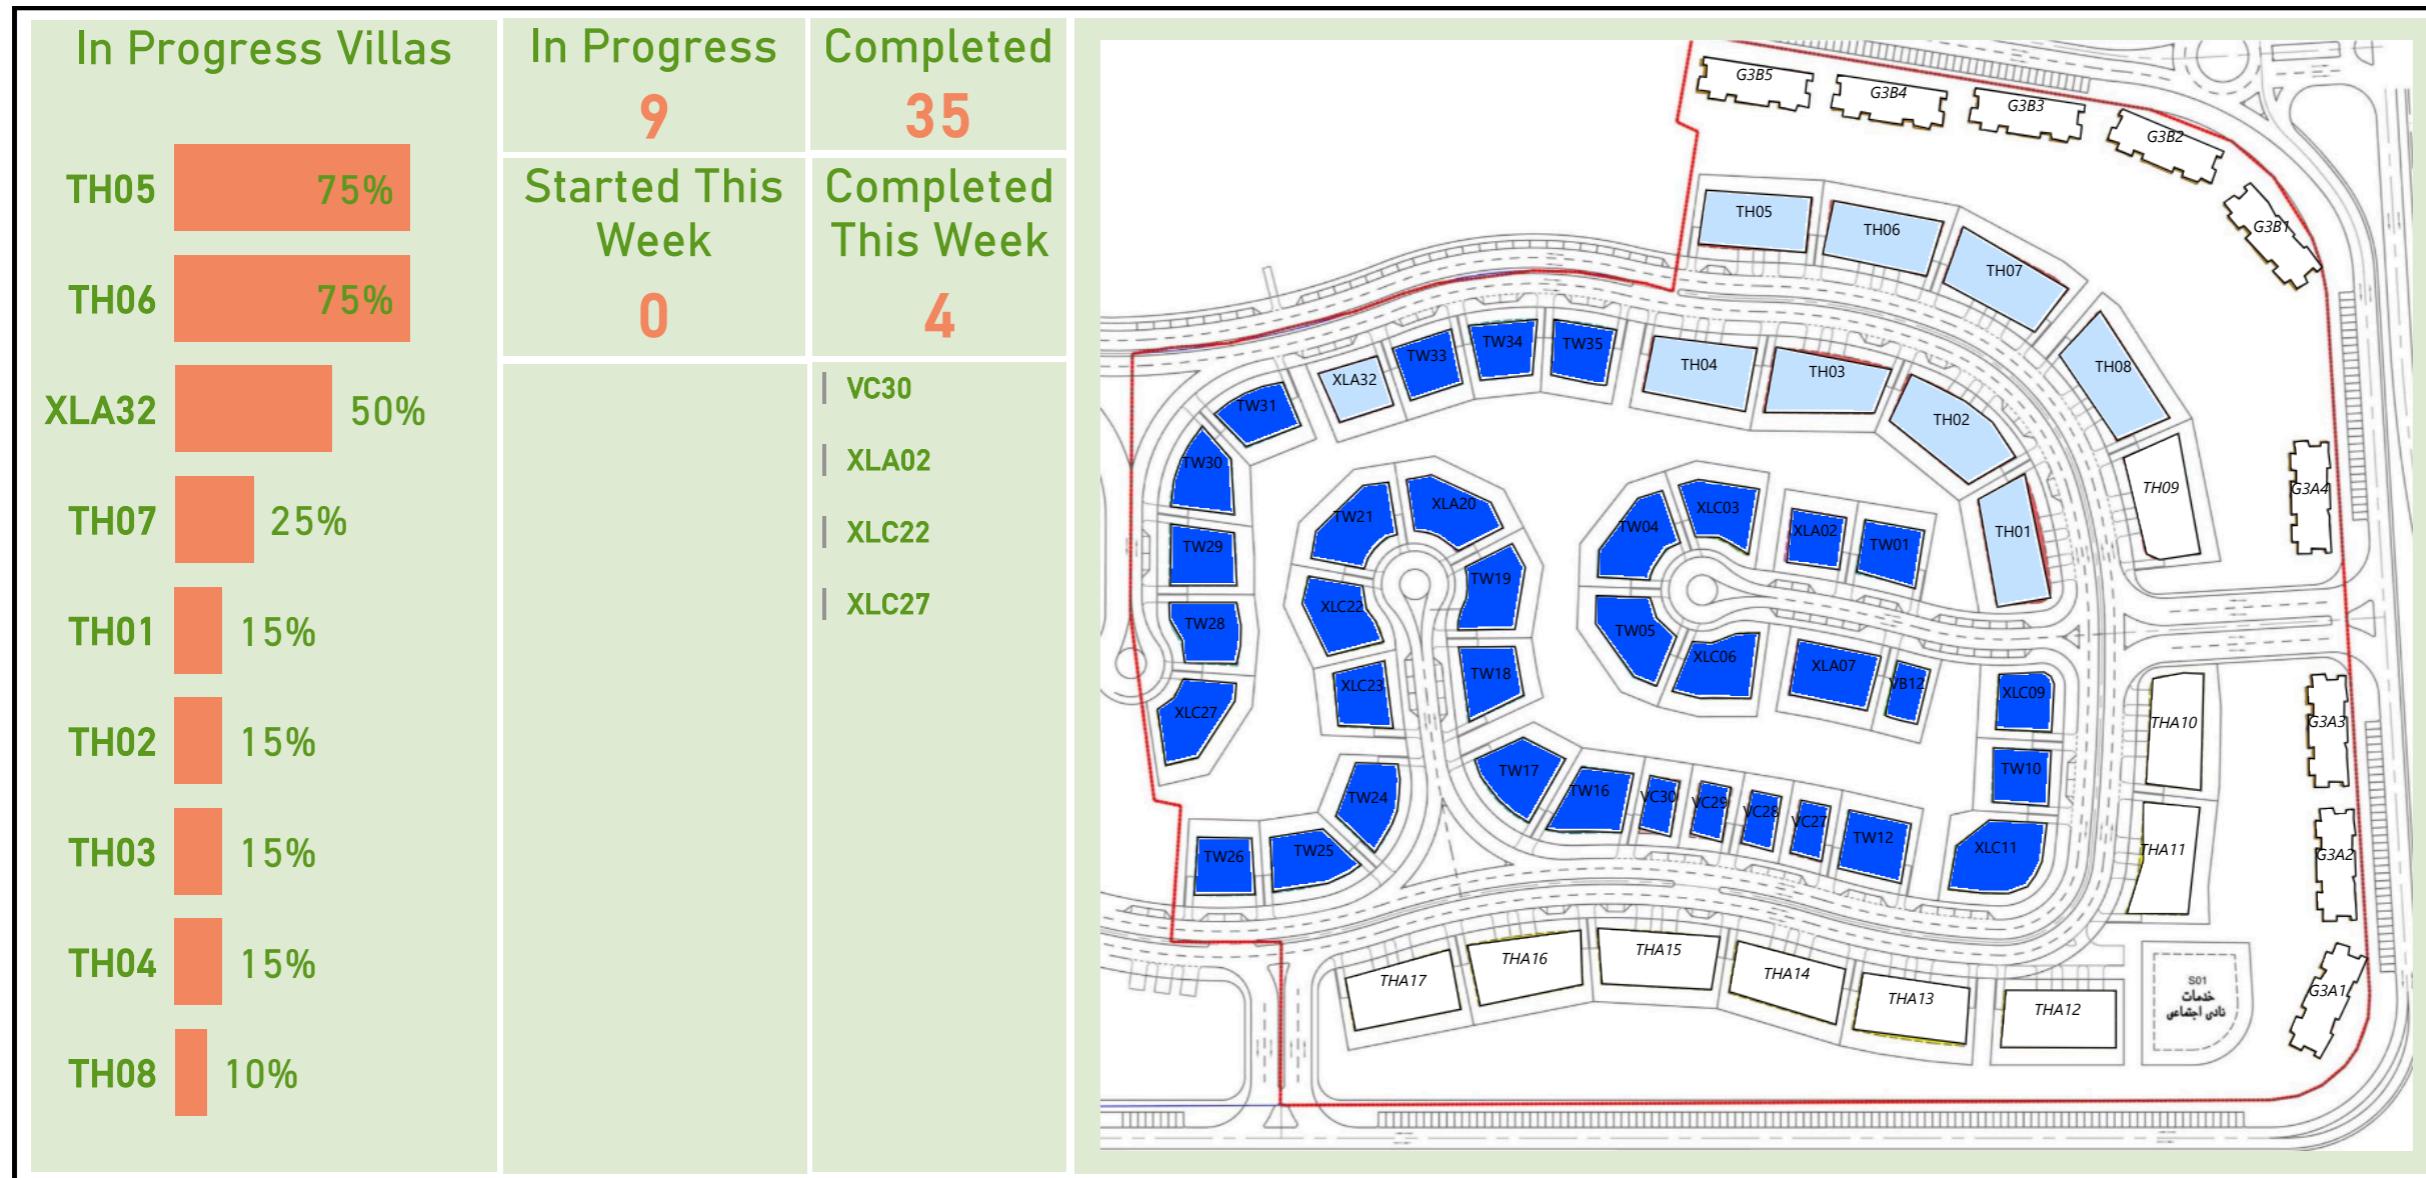


Activity

- Marble.FF Wet
- Marble.GF Reception
- Marble.Stone Vanity
- Other.EPS
- Other.External Wooden Doors
- Other.Internal Wooden Doors
- Other.Internal Wooden Doors
- Hardware
- Other.Stair Handrail
- Other.Steel Hook
- Painting.FF 1st
- Painting.FF Final
- Painting.GF 1st
- Painting.GF Final
- Plaster.FF 1st
- Plaster.FF Fill DRY
- Plaster.FF Fill WET
- Plaster.GF 1st
- Plaster.GF Fill DRY
- Plaster.GF Fill WET
- Tiles.FF HDF
- Tiles.FF Porcelain Wet
- Tiles.FF Tiles under HDF
- Tiles.GF Porcelain Wet
- Tiles.GF Tiles Dry
- Tiles.GF Tiles Wet

Data Date :
Saturday, March 08, 2025

Unit No.									Discipline	
Building #1	Building #2	Building #3	Building #4	Building #5	Building #6	Building #7	Building #8	Building #9	Fences	Finishes

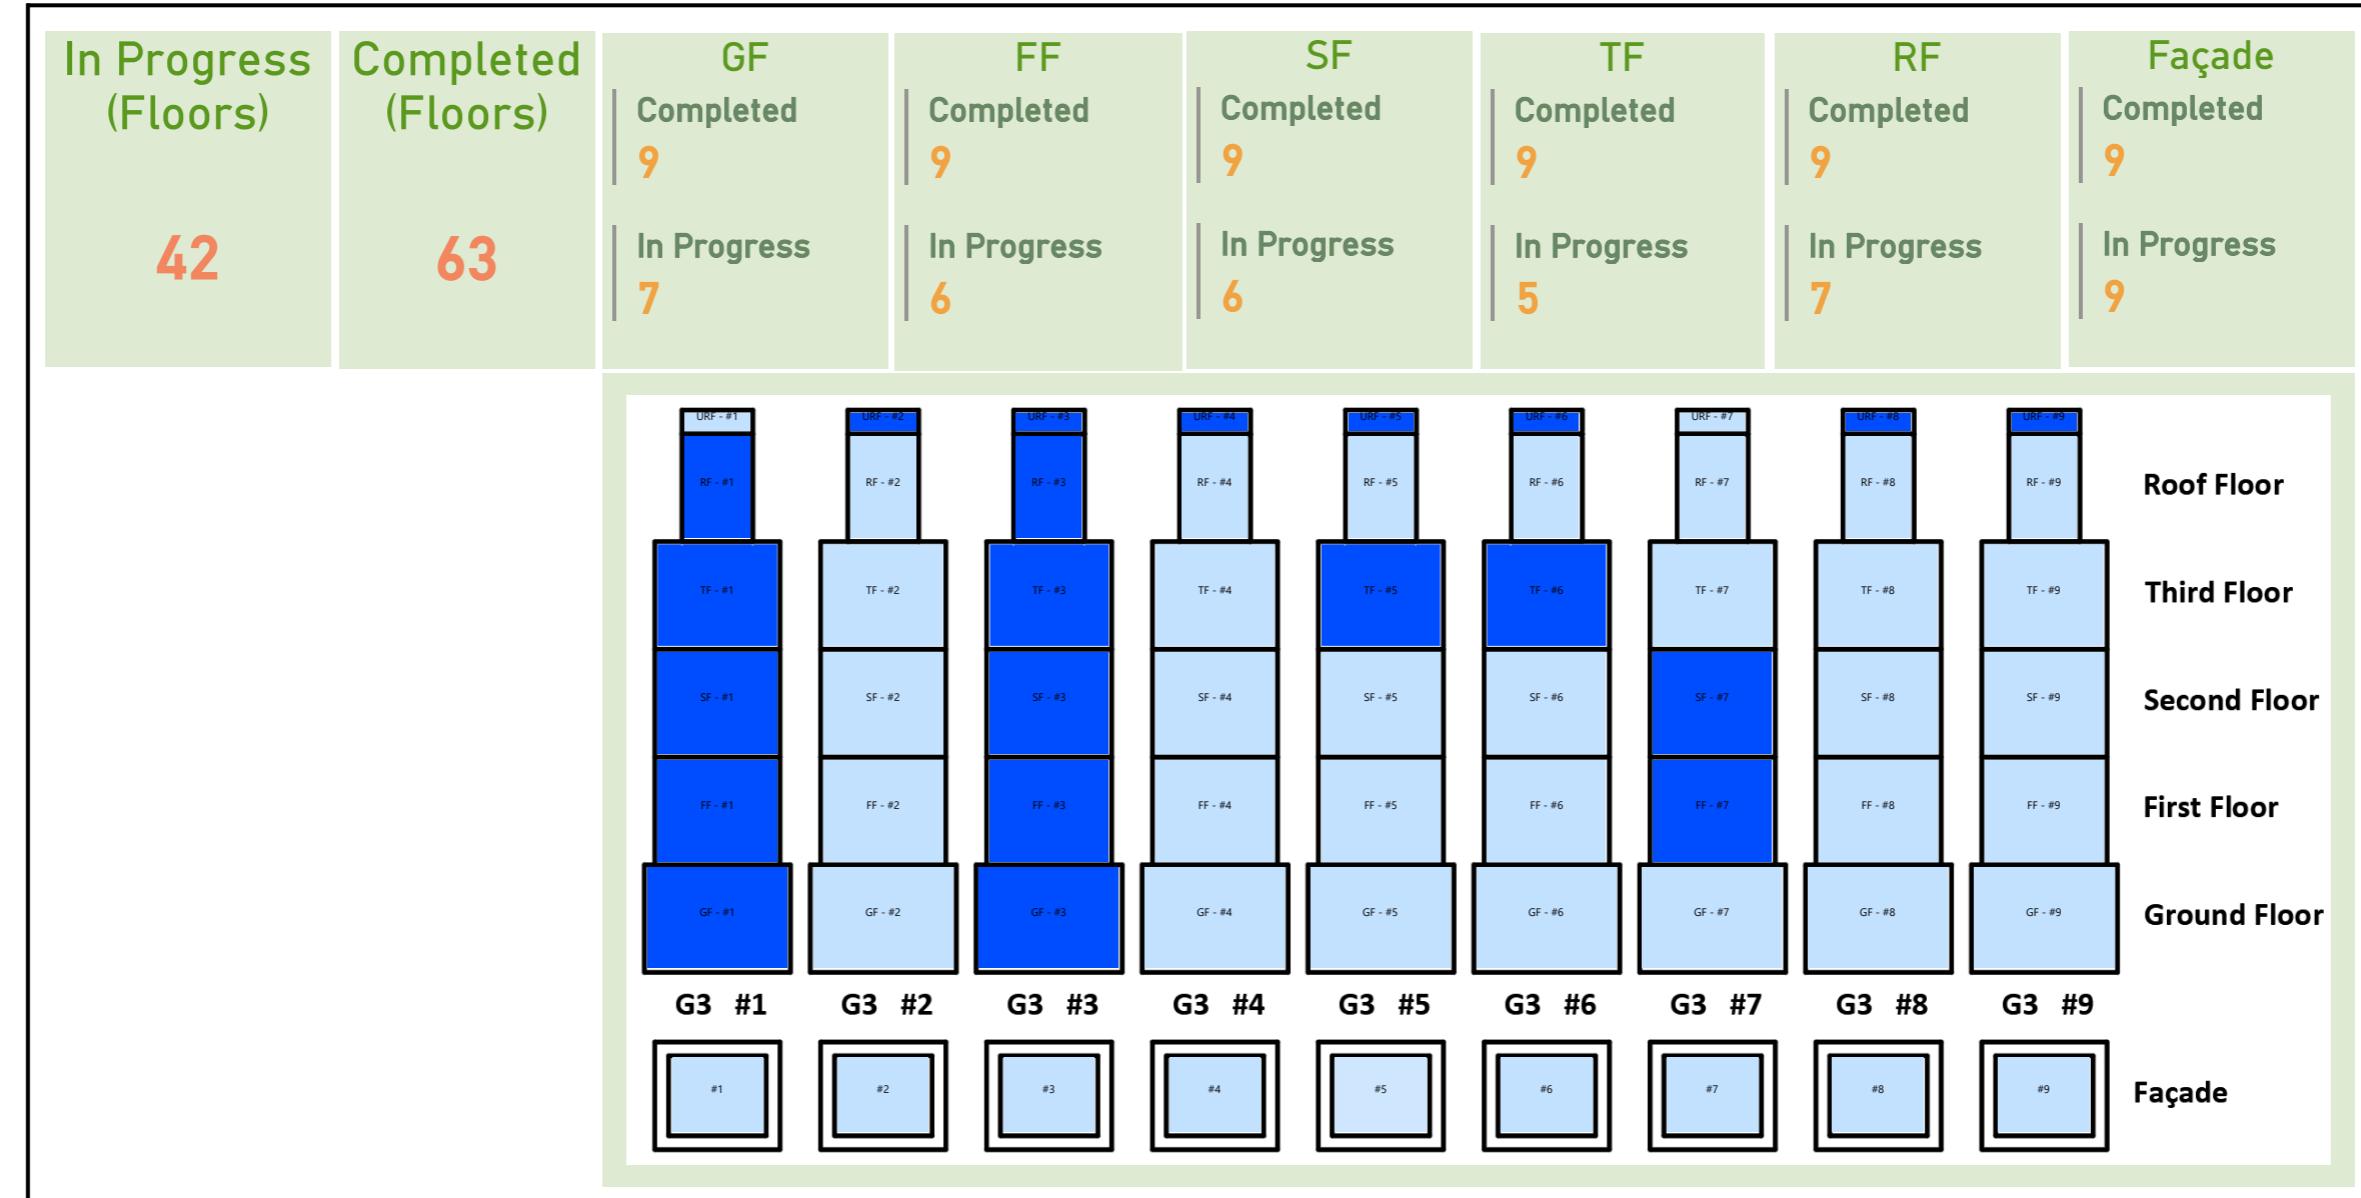

Activity
Doors . Internal
Doors . Metal Doors
EX . Dry Mix
EX . External Painting
EX . External Plaster
EX . Hashma 1st
EX . Hashma Final
EX . Stairs Handrail
EX . Terrace Handrail
Flooring . Ceramic Maid Room
Flooring . Ceramic Tiles Wet Area
Flooring . Ceramic under HDF
Flooring . Ceramic Walls Wet Area
Flooring . HDF
Flooring . Marble Dry Area
Flooring . Marble External Stairs
Flooring . Marble Terraces
Flooring . Porcelain Kitchen
Flooring . Porcelain Wet Area
Flooring . Terrace Water Proofing
Flooring . Vanity
Flooring . Wet Area Water Proofing
Gypsum . 1st
Gypsum . Final
Gypsum . Final Wet
Insulation . Aggregate
Insulation . Block Work
Insulation . Mineral Wool




Marassi S2
Progress Summary (B10 , B11 , B12)

marassi
مَرَّاسِي


Data Date
Tuesday, September 12, 2023

10	11	12	-1	0	1	2	3	4	5	Block	MEP	Paint	Plaster
----	----	----	----	---	---	---	---	---	---	-------	-----	-------	---------

Block Work Progress By Date

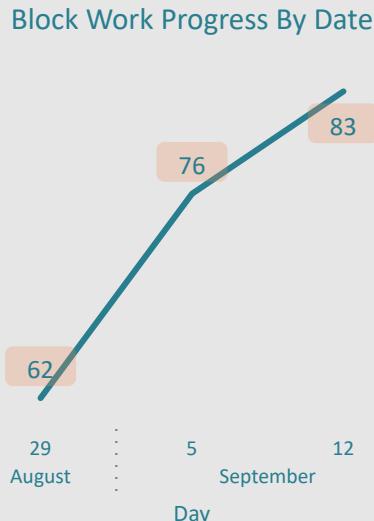

MEP Work Progress By Date

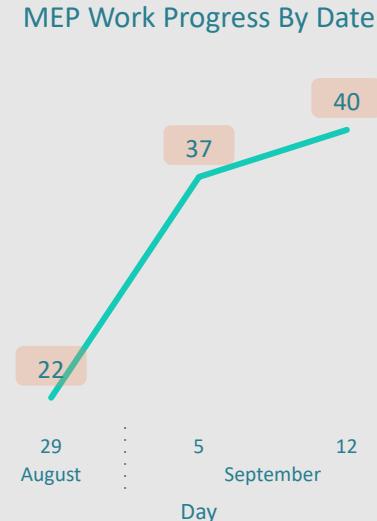



Plaster Work Progress By Date




Painting Work Progress By Date



Paint

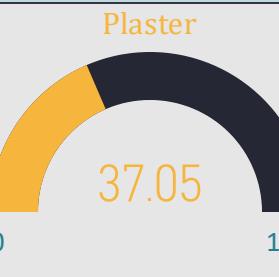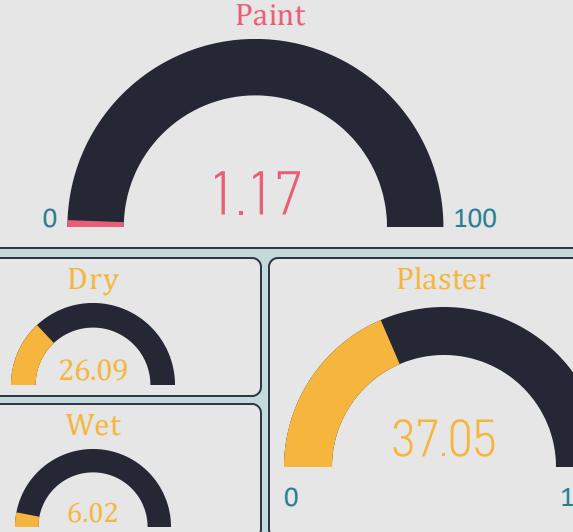

Progress By Trade (B10)

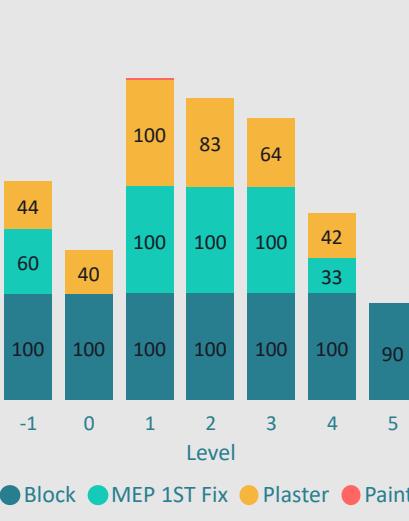


Progress By Trade (B11)




Progress By Trade (B12)




Average of % by Trade

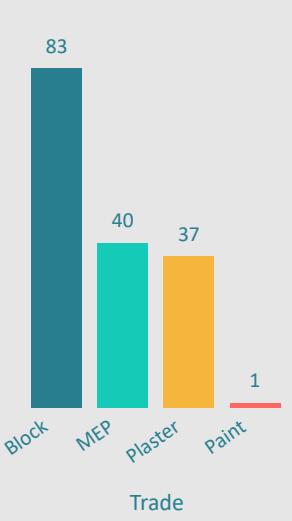

MEP 1ST Fix

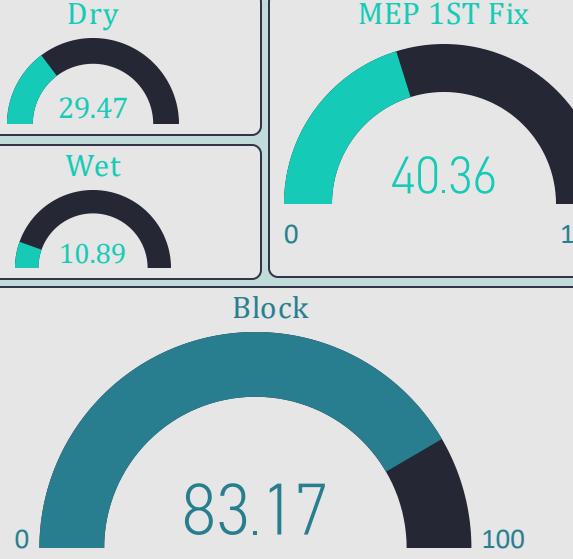

Block

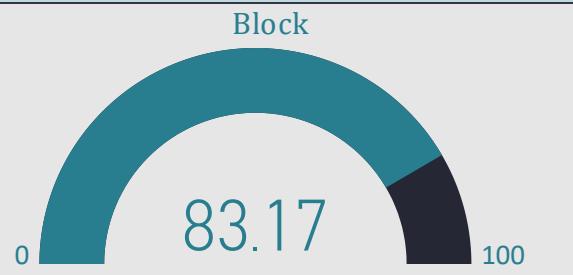


Group Number

1	2	3	4	5
1	3	7	9	11
2	4	8	10	12

Floor

#1	#4	RF
#2	GF	
#3	LGF	

Division

1	7	14	27
3	8	21	28
4	9	22	31
5	10	23	33
6	12	26	

Building Type

T1CN	T1EX	T2EX
T1CR	T2CX	
T1E	T2E	



KPI


WPC decking
Wooden doors
Windows
Waterproofing works for terraces's
Waterproofing membrane for roof
Waterproofing for Brick Works under SOG
Vinyl
underground cables
Toilets cabinets
Tiles
Stone cladding & Coping for external walls
Steel ladder
Steel handrails
Steel doors
Stair nosing
Stainless Steel floor Trim
Slopped Foam Concrete for roof
Signage
Shower Glass/HPL partitions
Screeding
Scaffolding
Roof Drain Works
Polyurethan coating for slab edge at roof
Polyeystrene foam Thermal Insulation

Sunday, August 08, 2021
Earliest Start


Friday, August 16, 2024
Latest Finish

Sunday, August 08, 2021
Earliest Actual Start

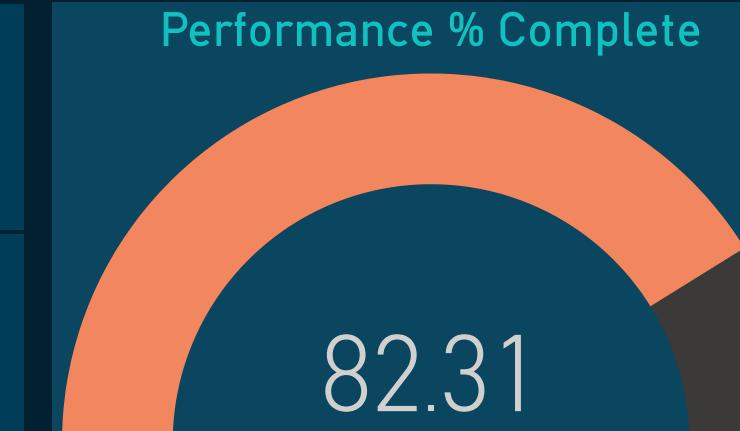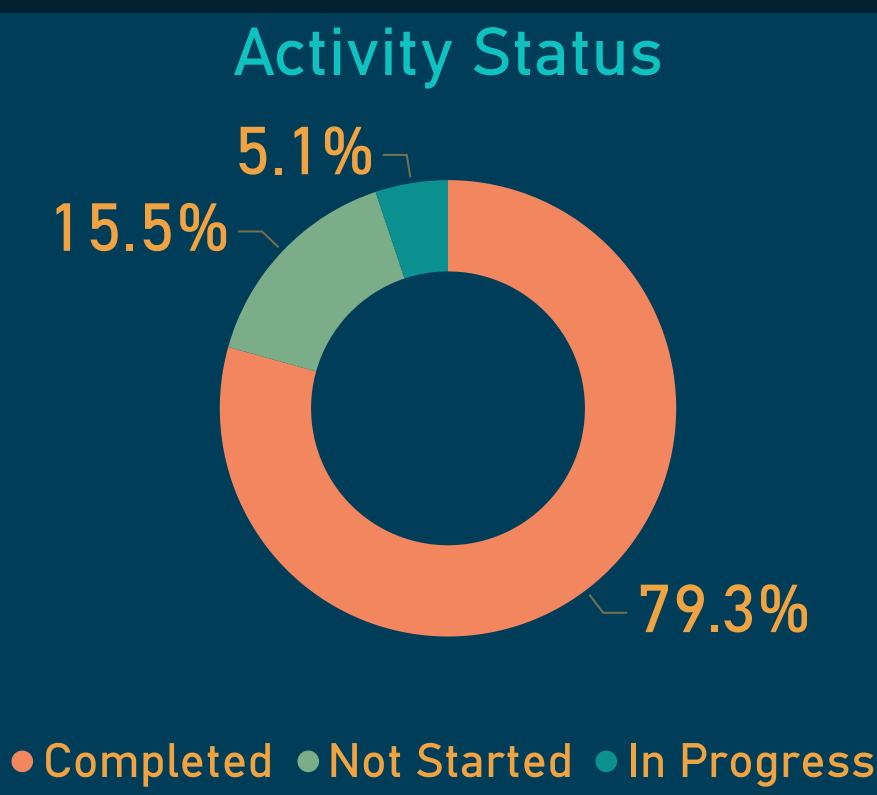Thursday, September 14, 2023
Latest Actual Finish

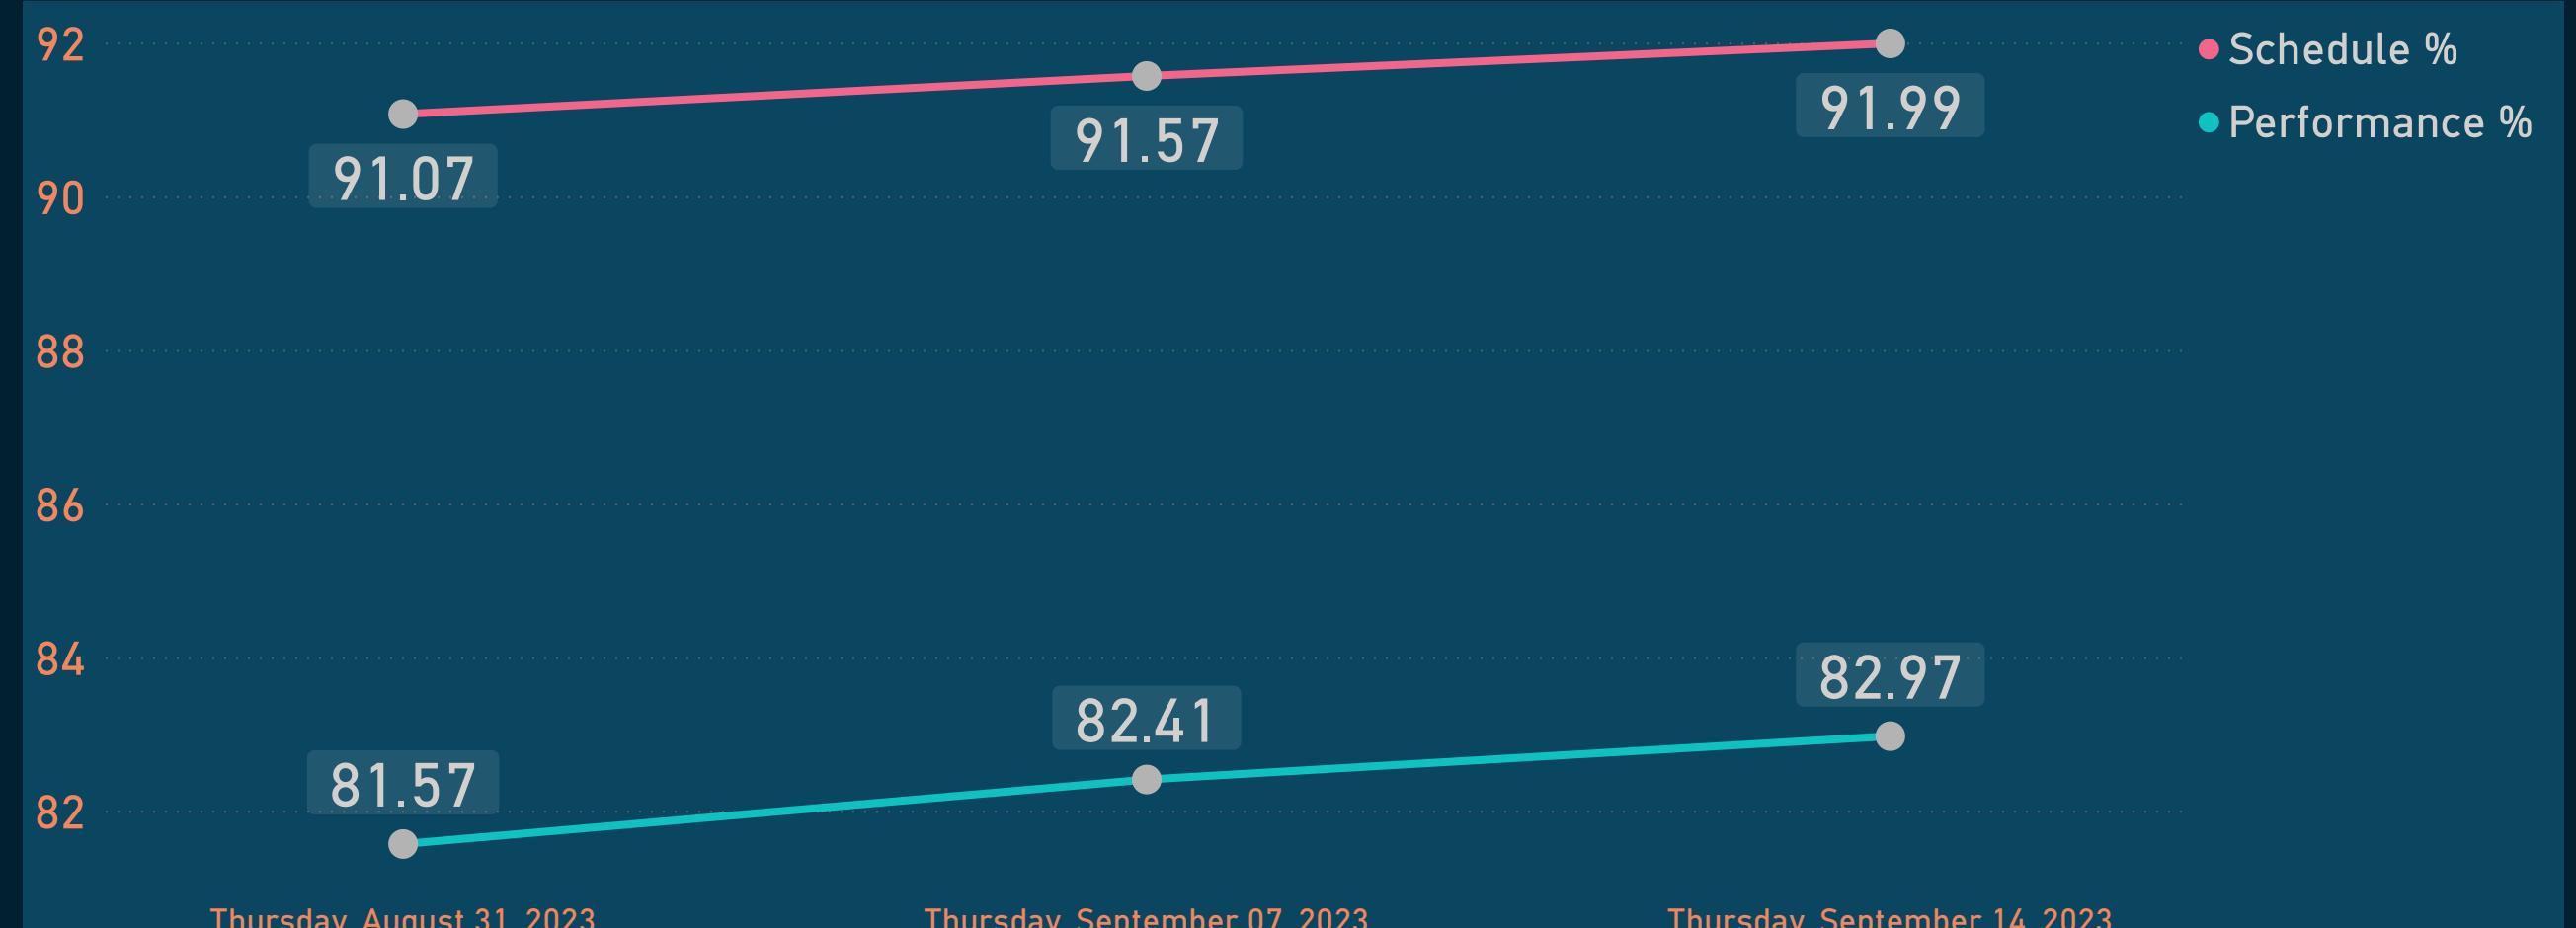Not Started Activity: **1248** In Progress Activity: **413** Completed Activity: **6376**

Earned Value Cost: **791.25M** **Budgeted Total Cost**: **970.87M**

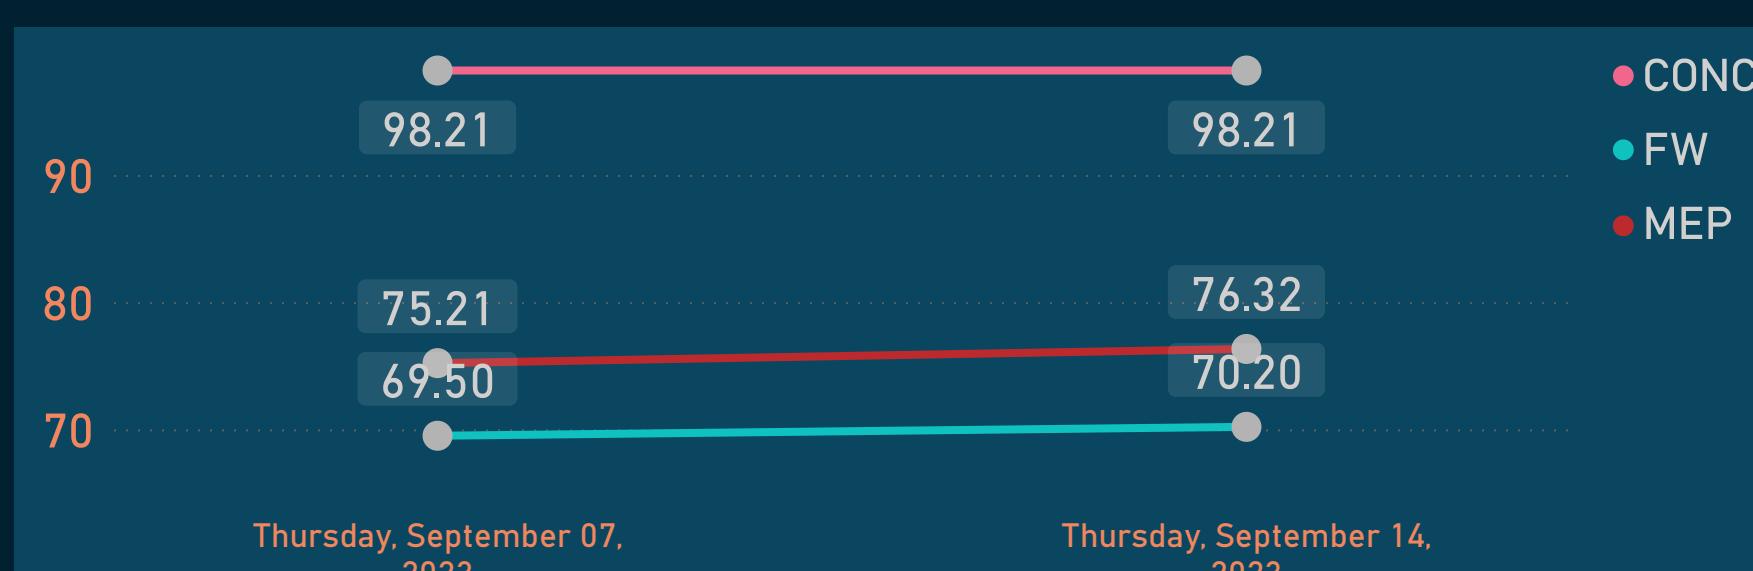Original Duration: **481** Actual Duration: **714**

Activity ID **Activity Name** **Original Duration(d)** **Schedule % Complete(%)** **Performance % Complete(%)** **Activity Status** **Total Float(d)**

Activity ID	Activity Name	Original Duration(d)	Schedule % Complete(%)	Performance % Complete(%)	Activity Status	Total Float(d)
A1030	Mobilization works	22	100	100	Completed	
A1040	Demobilization works	20	0	0	Not Started	-145
A1050	Construction of mockup appartement	90	100	100	Completed	
BA-GR-01	General Requirements	709	100	97	In Progress	-93
BB-GR-01	General Requirements	915	80	85	In Progress	-145
CON-CB-S1-01	Rain Water Drainage (catch basin, pipes)	7	100	100	Completed	
CON-CB-S2-01	Rain Water Drainage (catch basin, pipes)	7	100	100	Completed	
CON-CB-S3-01	Rain Water Drainage (catch basin, pipes)	7	100	100	Completed	



Data Date

Tuesday, September 12, 2023

Building No.






10


AACC
 ARABIAN CONSTRUCTION CO.






 marassi
 مراسى

Block	MEP 1st Fix Dry	MEP 1st Fix Wet	Dry Spot	Wet Spot	PLST PRP Dry	PLST PRP Wet	Fiber Dry	Fiber Wet	Filling Dry	Filling Wet
98.57	65.08	42.86	85.71	85.71	85.71	85.71	71.43	42.86	41.27	22.22





Roof



4th



3rd



2nd



1st



GF



LGF



Data Date

Tuesday, September 12, 2023

Building No.





11


AACC
 ARABIAN CONSTRUCTION CO.




marassi
 مراسى

Block	MEP 1st Fix Dry	MEP 1st Fix Wet	Dry Spot	Wet Spot	PLST PRP Dry	PLST PRP Wet	Fiber Dry	Fiber Wet	Filling Dry	Filling Wet
80.63	66.67	34.92	71.43	71.43	77.78	71.43	42.86	28.57	37.78	25.40





Roof



4th



3rd



2nd



1st



GF



LGF



Data Date

Tuesday, September 12, 2023

Building No.




12


AACC
 ARABIAN CONSTRUCTION CO.





 marassi
 مراسى

Block	MEP 1st Fix Dry	MEP 1st Fix Wet	Dry Spot	Wet Spot	PLST PRP Dry	PLST PRP Wet	Fiber Dry	Fiber Wet	Filling Dry	Filling Wet
68.15	10.00	0.00	23.33	16.67	23.33	16.67	6.67	0.00	0.00	0.00




Roof








4th









3rd







2nd



1st



GF



Cluster No.	Building Bo.	Trade	Sub-Contractor	Date	Date	Avg / Day
All	All	All	All	This - Year 1/1/2023 - 12/31/2023	All	84.5

No. Of Sub-Contractors

42


No. Of Item

21

Total Numbers

1775

No. By Date

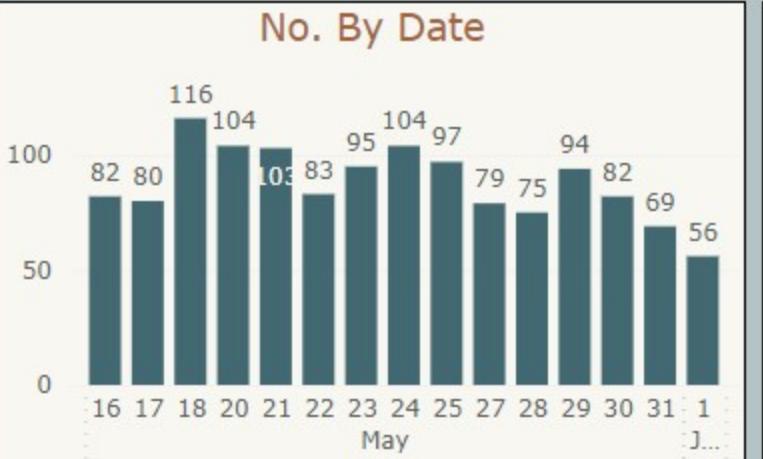


No. By Engineer



No. By Sub-Contractor




No. By Clusters

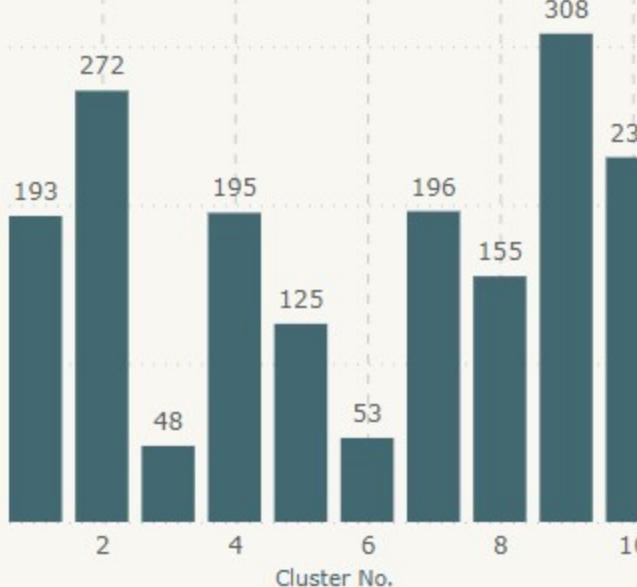

Total Numbers

TRADE	1	2	3	4	5	6	7	8	9
GRC	184	164		104		42	55	66	238
GRG					4	8	14		
المنور						9			
بانط اسطع		2	2						
بناء				14		5	15		
حدار									
رخام									
زجاجة									
ستلات									
سقف مطبخ				1					
سيراميك								2	
عامل بياضن		9	70	9	37	96	12		
عزل اسطح					4				
عزل خدمات						2			
Total	193	272	48	195	125	53	196	155	308

Sub-Contractor By Cluster

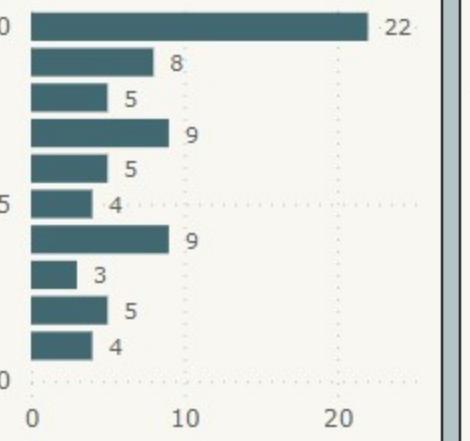

No. By Trade



No. By Cluster



HOME

Cluster No.

All

Building No.

All

Trade

All

Sub-Contractor

All

Date

All

First / Replaced

Daily

No. Of Engineers

13

No. Of Clusters

10

No. Of Trades

20

No. Of Sub-Contractors

42


No. Of Sub-Contractors By Trade



No. Of Trades By Engineers



تسكين بدل مقاول اخر ● بداية أعمال

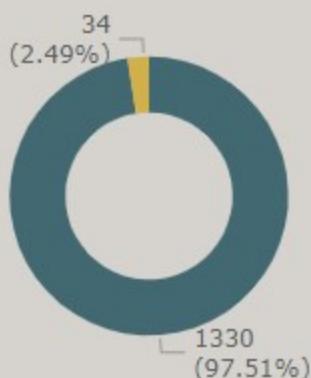

No. Of Trades By Cluster / Building

Bulding \ Location	1	2	3	4	5	6	7	8	9	10	Total
1	2	3	5	7	1	1	5	6	5	13	
1st	1	3	3	5	1	1	5	1	2	9	
2nd	1	3	5	5	1	4	1		2	9	
3rd	1	3	4	5	1	1	5	1	2	9	
4th	1	3	4	5	1	1	5	1	1	9	
5th	1	3	4	4		1	4	1	4	9	
6th	1	3	4	3		1	4	1	3	7	
7th	1	3	4	4		1	5	1	3	9	
8th							2		2		
9th								2		2	
B1	3	3	2				3	5		6	
B2	3	3	2				3	5		6	
Entrance	1	3					3	5		6	
GF	3	3	2		1	3	4		6		
H									2	2	
H1	1	3					3	1		3	
H2	1	3	11	1	1	6	1	13	20		
Total	3	4	5	11	1	1	6	1	13	20	

No. Of Trades By Sub-Contractors



% Progress



No. Of Activities By Cluster / Building

رقم العمارة	1	2	3	4	5	6	7	8	9	10	
1	13	82	51	46	3	9	111	43	21		
1st	1	6	4	5	1	1	8	1	2		
2nd	1	7	6	5		1	7	1	2		
3rd	1	6	5	5	1	1	8	1	2		
4th	1	6	5	5	1	1	8	1	1		
5th	1	6	5	4		1	7	1	4		
6th	1	6	5	3		1	7	1	3		
7th	1	6	5	4		1	8	1	3		
8th							2				
9th							2				
B1	4	4	2				6	5			
B2	4	4	2				6	5			
Entrance	1	3					3	6			
GF	5	4	2		1	6	5				
H									2		
H1	1	3					6	1			
Total	57	468	88	182	3	17	334	43	2	170	

HOME

Cluster No.

Building Bo.

Trade

Sub-Contractor

Date

First / Replaced

Daily


No. Of Sub-Contractors By Trade



No. Of Trades By Engineers



● شكين بدل مقاول اخر ● بداية اعمال

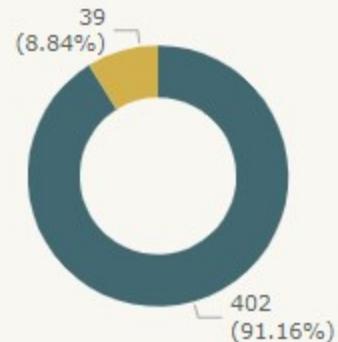

No. Of Trades By Cluster / Building

رقم العقارية	1	2	3	4	5	6	7	8	9	10	Total
1	1	2	2	2	3	1	5	2	1	3	7
2	1	2	2	2	3	4	2	1	3	7	7
3	1	2	2	2	2	1	4	2	1	3	7
4	1	2	2	2	2	4	2	1	2	7	7
5	1	2	2	2	2	5	2	1	3	7	7
6	1	2	2	2	2	4	2	1	3	7	7
7	1	2	2	2	3	4	2	1	3	7	7
8								1	1		1
9								1	1		1
10								1	1		1
2	1	2	2	3		5	2	5	7		
1	1	2	2	2		5	2	4	7		
2	1	2	2	2		5	2	4	7		
3	1	2	2	2		4	2	5	6		
4	1	2	2	2		4	2	5	6		
5	1	2	2	2		4	2	4	6		
Total	2	2	2	3	3	2	6	2	2	6	9

No. Of Engineers

10

No. Of Clusters

10

No. Of Trades By Sub-Contractors



Location Of Work By Cluster



No. Of Activities By Cluster / Building

رقم العقارية	1	2	3	4	5	6	7	8	9	10	Total
1	7	14	14	14	17	1	29	14	7	23	
2	1	2	2	2	3	4	2	1	4	4	
3	1	2	2	2	2	1	4	2	1	3	
4	1	2	2	2	2	4	2	1	2	2	
5	1	2	2	2	2	5	2	1	3	3	
6	1	2	2	2	2	4	2	1	3	3	
7	1	2	2	2	3	4	2	1	3	3	
8								1			
9								1			
10								1			
2	5	12	12	13		26	10	25			
1	1	2	2	2		5	2	5			
2	1	2	2	2		5	2	5			
3	1	2	2	2		4	2	5			
4	1	2	2	2		4	2	5			
5	1	2	2	2		4	2	5			
Total	24	44	26	59	17	14	112	14	53	78	

No. Of Trades

9

No. Of Sub-Contractors

25

HOME

Cluster No.	Part No.	Type	Final	Submitted Date
CL10	All	AR	All	All

Daily

Create By	Level	Trade	Action	Approving Date
All	All	All	All	All

Internal

Total Submittals	Under Reviewing	Avg. Reviewing Duration	No. Of Creator
267	4	23	19

External

Total DWGs	Approved DWGs	First Time Approvals	Rejected
1,759	1,659	1,204	94

TO-SD

No. Of Shop-Drawings By Submitted Date

Year	No. Of Shop-Drawings
2019	86
2020	51
2021	100
2022	53
2023	25

TO-QS

No. Of Shop-Dr Date

Year	No. Of Shop-Drawings
2019	74
2020	60
2021	98
2022	56
2023	23

TO-MIR

No. Of Shop-Dr Date

Year	No. Of Shop-Drawings
2019	74
2020	60
2021	98
2022	56
2023	23

QC-Internal

No. Of Shop-Dr Date

Year	No. Of Shop-Drawings
2019	74
2020	60
2021	98
2022	56
2023	23

Inventory

No. Of Shop-Dr Date

Year	No. Of Shop-Drawings
2019	74
2020	60
2021	98
2022	56
2023	23

KPI

94.6

Classification Of Submittals

جنة الإعداد	الإجمالي
ذاتي	215
DESIGNERS	25
Sub-Contractor	14
CCG	4
CCG 35%	4
CCG 35%	3
CCG	2
Total	267

No. Of Submittals By Cluster


Cluster	No. Of Submittals
CL10	267
TILES	88
Block Work	715
48	286
FALSE CEILING	29
107	151
ELEVATIONS	26
151	124
GRC	26
14	124

All Actions

Action	No. Of Actions
B	14
B/C	124
C	124

Detailed Data By (Date & Sub No. & DWG No.) And Rev. No.

تاريخ الإعداد	0	1	2	3	4
Wednesday, April 05, 2023	SD-R5-Z8-AR-1577	R5-Z8-TY(H)-TL-AR-2435H	✓		
		R5-Z8-TY(H)-TL-AR-2436H	✓		
		R5-Z8-TY(H)-TL-AR-2437H	✓		
SD-R5-Z8-AR-1580	R5-Z8-TY(C)-TL-AR-2432C	✓			
	R5-Z8-TY(C)-TL-AR-2433C	✓			
	R5-Z8-TY(C)-TL-AR-2434C	✓			
Sunday, April 02, 2023	SD-R5-Z8-AR-1584	R5-Z8-CL10-HR-AR-12013	✓		
	R5-Z8-CL10-HR-AR-12014	✓			
	R5-Z8-CL10-HR-AR-12015	✓			
	R5-Z8-CL10-HR-AR-12016	✓			
Tuesday, March 28, 2023	SD-R5-Z8-AR-1574	R5-Z8-TY(K)-TL-AR-2143K	✓		
	R5-Z8-TY(K)-TL-AR-2144K	✓			
	R5-Z8-TY(K)-TL-AR-2145K	✓			

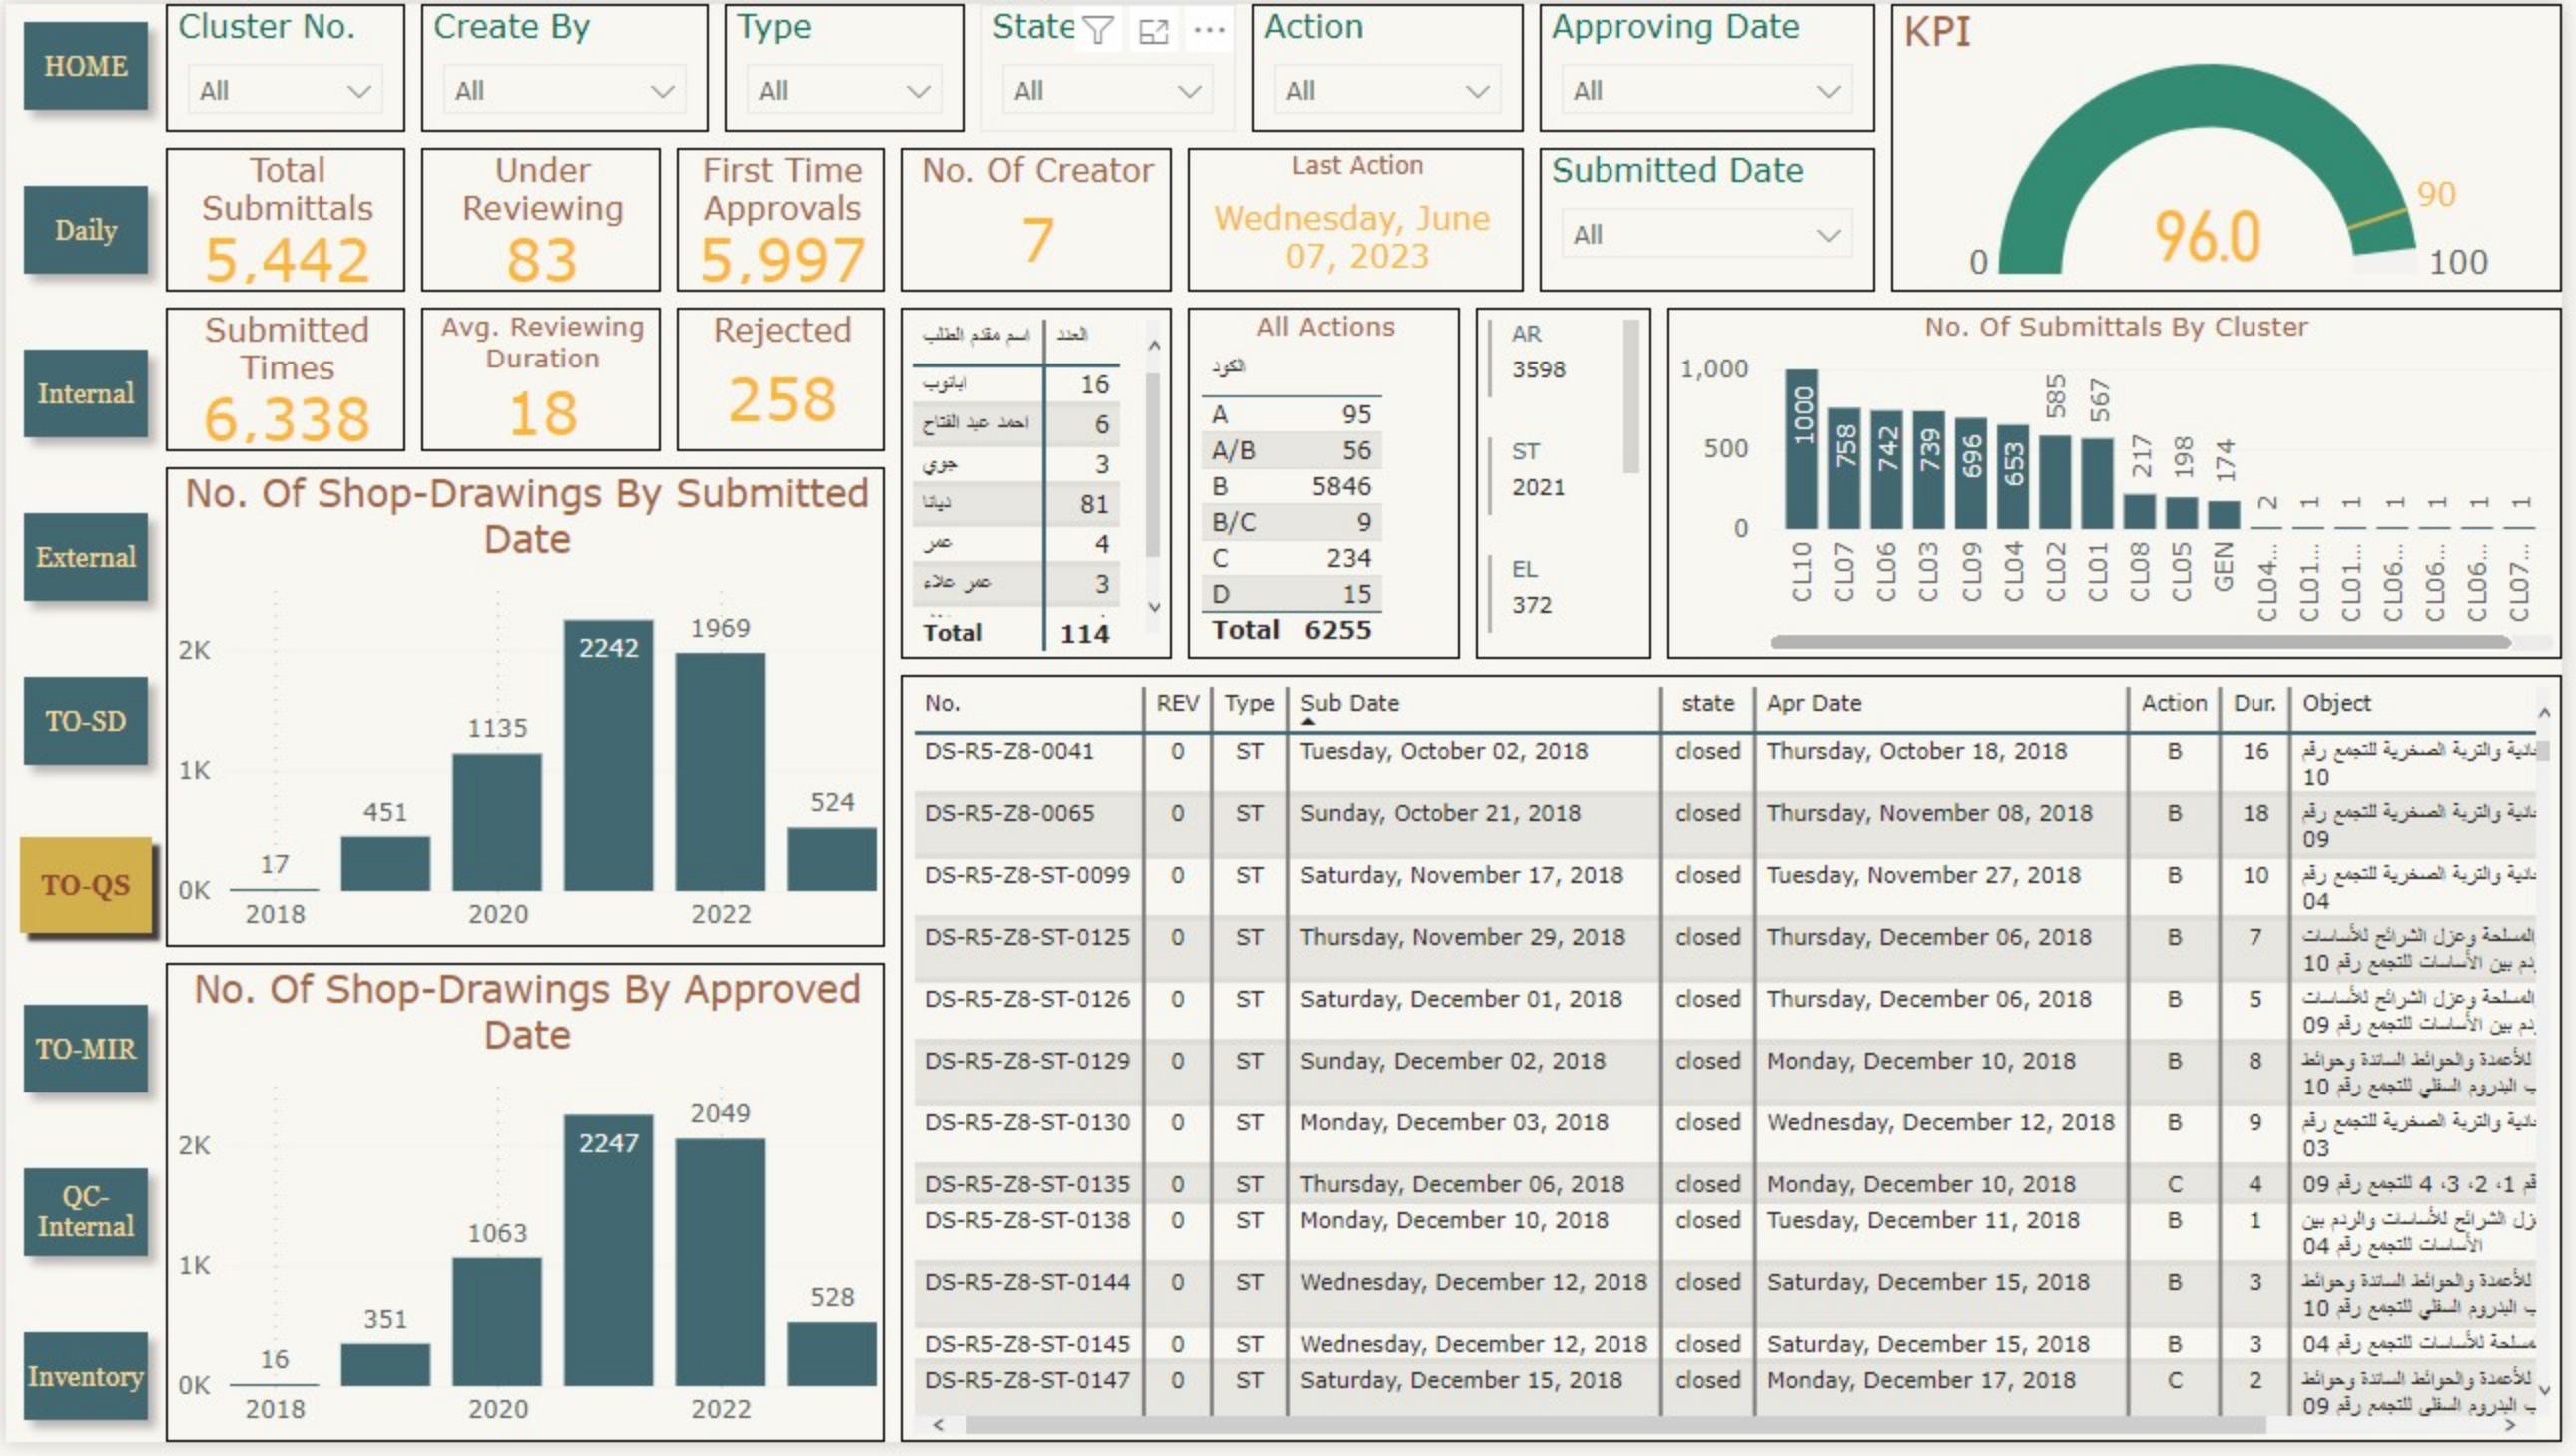

HOME

Cluster No.

Daily

Total Submittals
706
Approved Submittals
566
First Time Approvals
506
Suppliers
29
Under Reviewing
12
Rejected
360
Avg. Reviewing Duration
14

No. Of Shop-Drawings By Submitted Date



No. Of Shop-Drawings By Approved Date



Submitted Date

Approving Date

All Actions

- A/C
- B
- B/C
- B/D
- C
- D

Supplier

AR	330
ME	146
ST	105
EL	90
FSIME	3
فني جرده محمد المصطفى المقفارات	3
LARA	2
NEW TEC	2
ME INF	32
TOSHKA	2
EL INF	11

Submittal

Rev

Submittal	Rev
MT-R5-Z8-ME-055	5
MT-R5-Z8-AR-089	4
MT-R5-Z8-ME-032	4
MT-R5-Z8-ME-034	4
MT-R5-Z8-ME-058	4
MT-R5-Z8-AR-048	3
MT-R5-Z8-AR-094	3
MT-R5-Z8-AR-100	3
MT-R5-Z8-AR-158	3
MT-R5-Z8-AR-159	3
MT-R5-Z8-AR-162	3
MT-R5-Z8-AR-314	3
MT-R5-Z8-INF-EL-0003	3
MT-R5-Z8-LS-S-0002	3
MT-R5-Z8-ME-082	3
MT-R5-Z8-005	2
MT-R5-Z8-016	2
MT-R5-Z8-017	2
MT-R5-Z8-025	2
MT-R5-Z8-026	2
MT-R5-Z8-029	2
MT-R5-Z8-030	2
MT-R5-Z8-AR-004	2
MT-R5-Z8-AR-006	2
MT-R5-Z8-AR-027	2
MT-R5-Z8-AR-031	2
MT-R5-Z8-AR-036	2
MT-R5-Z8-AR-046	2
MT-R5-Z8-AR-076	2
MT-R5-Z8-AR-084	2
MT-R5-Z8-AR-093	2
MT-R5-Z8-AR-095	2
MT-R5-Z8-AR-104	2
MT-R5-Z8-AR-106	2
MT-R5-Z8-AR-107	2
MT-R5-Z8-AR-128	2
MT-R5-Z8-AR-132	2
MT-R5-Z8-AR-139	2

KPI

KPI



Detailed Data By (Date & Sub No. & DWG No.) And Rev. No.

Year	0	1	2	3	4
2023					
May					
31					
MT-R5-Z8-LS-S-0003					✓
20					
MT-R5-Z8-ME-146					✓
MT-R5-Z8-EL-104					✓
17					
MT-R5-Z8-AR-323					✓
13					
MT-R5-Z8-AR-268					✓
11					
MT-R5-Z8-LS-S-0003					✗
April					
11					
MT-R5-Z8-EL-105					✓
MT-R5-Z8-AR-324					✓
8					
MT-R5-Z8-ME-145					✓

HOME

Cluster No.

Part No.

Type

Trade

Submitted Date

Daily

Create By

Reviewed By

Action

Approving Date

Internal

Total Inspections

42

Approved Inspections

37

Rejected Inspections

4

Open Inspections

1

Average Reviewing Inspection

1.17

الحالة	الجريدة	No.
Open	1	
Closed	B	37
Closed	C	4

Inspections By Construction Engineer




Inspections By QC Engineer




External

Inspections By Date

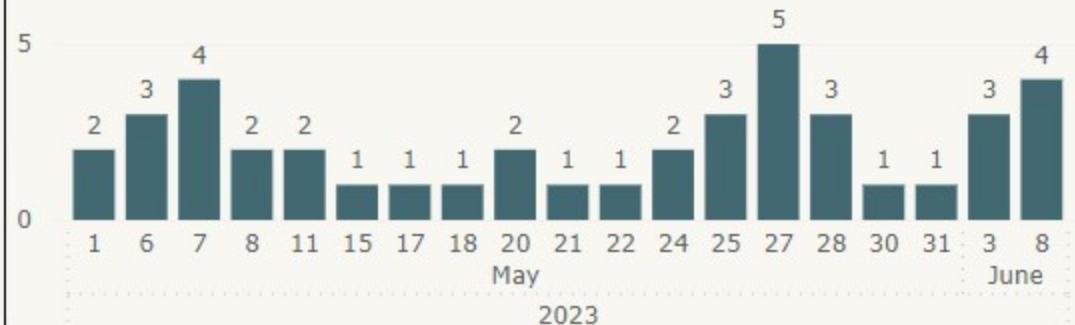

KPI

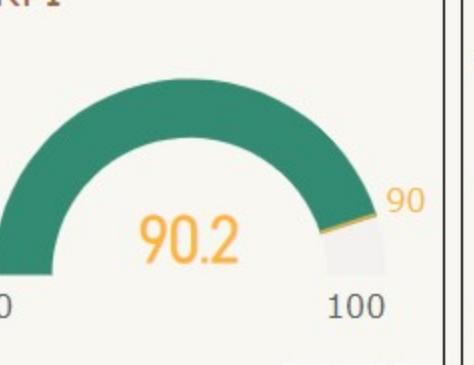


Inspections By Trade




TO-MIR

رقم	Rev	النوع	Submitted Date	رقم التجمع	رقم العماره	المكان	البلد	Action Time Stamp	الجريدة	الحالة	Duration	
	0	ARC	Thursday, June 08, 2023	2	4	8th	بياضن			Open		
	0	ARC	Thursday, June 08, 2023	7	2	Elev.4	قرميد	Thursday, June 08, 2023	B	Closed	1	
	0	ARC	Thursday, June 08, 2023	10	1	Elev 2 (سفل رخام)	رخام	Thursday, June 08, 2023	B	Closed	1	
6721	0	ARC	Monday, May 01, 2023	7	MZ	Plaza	عزل	EBDM	Tuesday, May 02, 2023	B	Closed	2
6722	0	ARC	Monday, May 01, 2023	7	MZ	Plaza	عزل	EBDM	Tuesday, May 02, 2023	B	Closed	2
6723	0	ARC	Saturday, May 06, 2023	10	1	منور	بياضن		Sunday, May 07, 2023	B	Closed	0
6724	0	ARC	Saturday, May 06, 2023	10	1	منور	دھانات		Sunday, May 07, 2023	B	Closed	0
6725	0	ARC	Saturday, May 06, 2023	10	2	5th	رخام		Sunday, May 07, 2023	B	Closed	0
6726	0	ARC	Sunday, May 07, 2023	10	4	GF	عزل حمامات		Monday, May 08, 2023	B	Closed	1

Inspections By Cluster

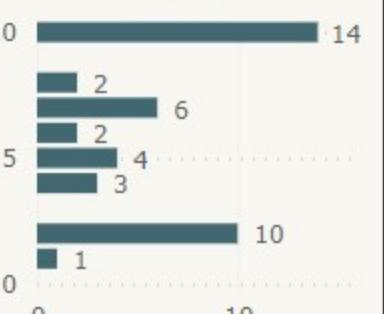

Inspections By Type

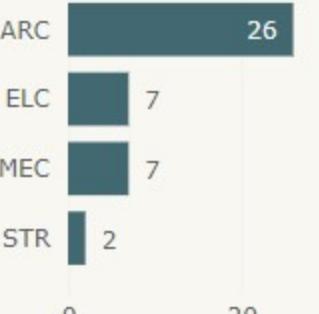

Inventory

HOME

Classification

Last Transaction date

Last Receive date

Earliest Receive Date

Last Receive Date

Daily

Total Types

20

Total Items

434

Total Items



Last Transaction date

9/16/2018

Last Receive date

9/16/2018

Earliest Transaction Date

Sunday, October 28, 2018

Last Transaction Date

Monday, May 01, 2023

Internal



TO-SD



Classification	QTY	Cost
سیر امريك	106	~10M
اجهزه صحية	29	~2M
حريق	48	~4M
فرمید	1	~0.1M
مواسير صحية	93	~9M
اکسووارات ابواب	8	~0.8M
كهرباء	54	~5M
ري	9	~0.9M
ادوات وعدد	18	~1.8M
صحي	22	~2.2M
حديد سلیج	5	~0.5M
تطبيقات	17	~1.7M
اسمنت	1	~0.1M
معدات	7	~0.7M
اخري	8	~0.8M
سولار	1	~0.1M
مياه	1	~0.1M
پلاستيك	3	~0.3M
Total	434	~35M

TO-QS



TO-MIR

QC-Internal

Inventory
